INDEX LEGEND

LOCATION:	SE1/4 - SEC. 28, T89N, R5W, NE1/4 - SEC. 33, T89N, R5W, SW1/4 - SEC. 27, T89N, R5W, NW1/4 - SEC. 34, T89N, R5W, SE1/4 - SEC. 27, T89N, R5W, NE1/4 - SEC. 34, T89N, R5W SW1/4 - SEC. 26, T89N, R5W, NW1/4 - SEC. 35, T89N, R5W, SE1/4 - SEC. 26, T89N, R5W, SW1/4 - SEC. 25, T89N, R5W, NE1/4 - SEC. 35, T89N, R5W, SE1/4 - SEC. 25, T89N, R5W, NW1/4 - SEC. 36, T89N, R5W, NE1/4 - SEC. 36, T89N, R5W, SW1/4 - SEC. 30, T89N, R4W, SE1/4 - SEC. 30, T89N, R4W, NW1/4 - SEC. 31, T89N, R4W, SW1/4 - SEC. 29, T89N, R4W, NE1/4 - SEC. 31, T89N, R4W, SE1/4 - SEC. 29, T89N, R4W, NW1/4 - SEC. 32, T89N, R4W, SW1/4 - SEC. 28, T89N, R4W, NE1/4 - SEC. 32, T89N, R4W, SE1/4 - SEC. 28, T89N, R4W, NW1/4 - SEC. 33, T89N, R4W, SW1/4 - SEC. 27, T89N, R4W, NE1/4 - SEC. 33, T89N, R4W SE1/4 - SEC. 27, T89N, R4W, NW1/4 - SEC. 34, T89N, R4W, SW1/4 - SEC. 26, T89N, R4W, NE1/4 - SEC.34, T89N, R4W, SE1/4 - SEC. 26, T89N, R4W, NW1/4 - SEC. 35, T89N, R4W, NE1/4 - SEC. 35, T89N, R4W FISHER SUBDIVISION, G. WALL FARMS SUBDIVISION AMENDED, BENNETT FAMILY SUBDIVISION, PILGRIM'S SUBDIVISION, HARDIN SUBDIVISION, DRY CREEK SUBDIVISION
REQUESTOR:	DELAWARE COUNTY ENGINEER
SURVEYOR:	BRAD J. BURGER
RETURN TO:	DELAWARE COUNTY ENGINEER'S OFFICE 2139 HIGHWAY 38, MANCHESTER, IOWA 52057 PHONE: 563-927-3505

Book 2020 Page 4780

Document 2020 4780 Type 06 001 Pages 12
Date 12/22/2020 Time 1:05:23PM
Rec Amt $.00

Daneen Schindler, RECORDER/REGISTRAR
DELAWARE COUNTY IOWA

Prepared by Brad Burger Delaware County Engineer's Office 2139 Highway 38, Manchester, Iowa 52057 Phone 563-927-3505


MONUMENT PRESERVATION CERTIFICATE

Procedure used to preserve the position of the monument:
The position of found monuments that were disturbed or removed during construction were preserved using GPS coordinates.

Coordinate System: Iowa State Plane, North Zone (1401), NAD83 (1996)

Public improvement project: P.C.C. OVERLAY ON COUNTY ROAD D22 (210TH STREET)
PROJECT NUMBER: STBG-SWAP-2197(601)--FG-28

LOCATION MAP FROM PROJECT PLANS – NO SCALE

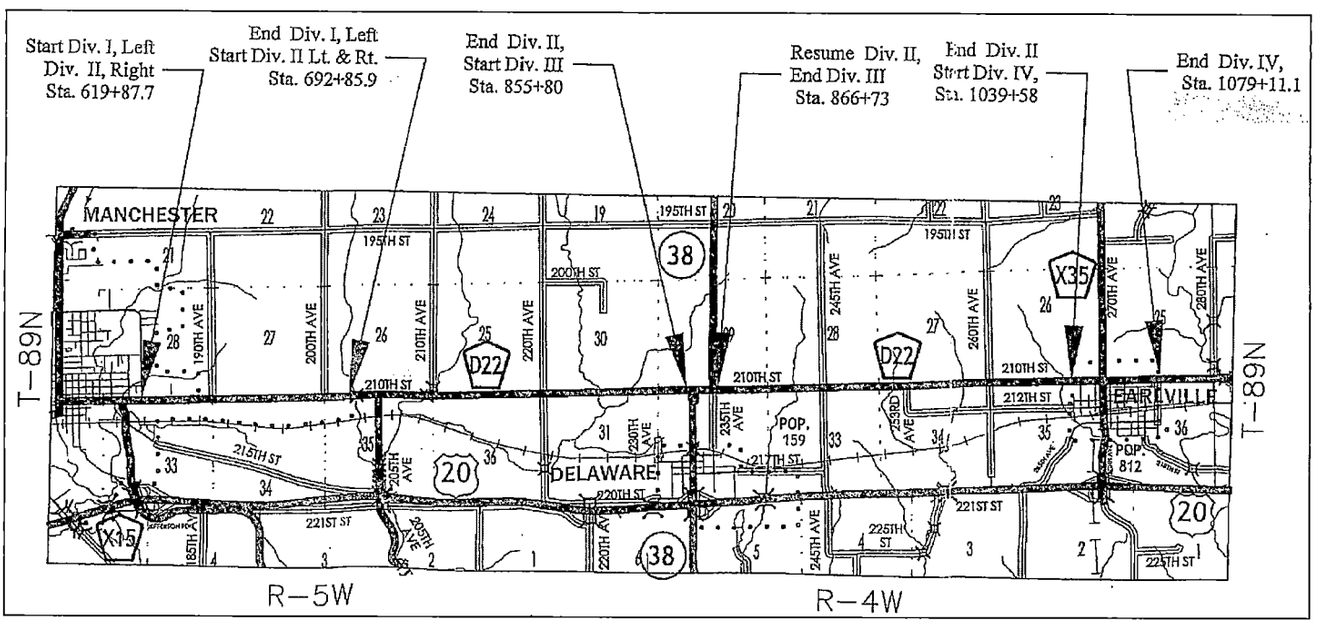

SEE SHEETS 2 - 12

LICENSED LAND SURVEYOR
BRAD J. BURGER
20281
IOWA

SHEET NO. 1-12 COVERED BY THIS SEAL

I HEREBY CERTIFY THAT THIS LANDSURVEYING DOCUMENT WAS PREPARED AND RELATED SURVEY WORK WAS PERFORMED BY ME OR UNDER MY DIRECT PERSONAL SUPERVISION AND THAT I AM A DULY LICENSED LAND SURVEYOR UNDER THE LAWS OF THE STATE OF IOWA. MY LICENSE RENEWAL DATE IS DECEMBER 31, 2020

Brad J. Burger 12/21/2020
BRAD J. BURGER #20281 DATE


Delaware County Engineer's Office
2139 Highway 38
Manchester, Iowa 52057

MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
1	MAG NAIL	CUT X	3646288.69	5478746.19
2	MAG NAIL	CUT X	3646300.76	5479105.83
3	MAG NAIL W/ CUT X	CUT X	3646310.94	5479408.18
4	MAG NAIL	CUT X	3646333.74	5480007.65
5	MAG NAIL	CUT X	3646342.37	5480231.38
6	MAG NAIL	CUT X	3646361.56	5480737.15
7	MAG NAIL W/ WASHER #17939	CUT X	3646362.36	5480757.11
8	MAG NAIL W/ WASHER #15525	CUT X	3646398.86	5481719.88
9	MAG NAIL	CUT X	3646412.10	5482066.11


LEGEND

- SECTION CORNER AS NOTED
- FD. MONUMENT AS NOTED IN TABLE, SET CUT X AFTER PROJECT
- FD. MONUMENT AS NOTED IN TABLE, SET MAG NAIL W/ WASHER AFTER PROJECT
- SECTION LINE AND OR 1/4 SECTION LINE
- LOT LINE OR PARCEL LINE
- MANCHESTER CITY CORP. LIMITS LINE

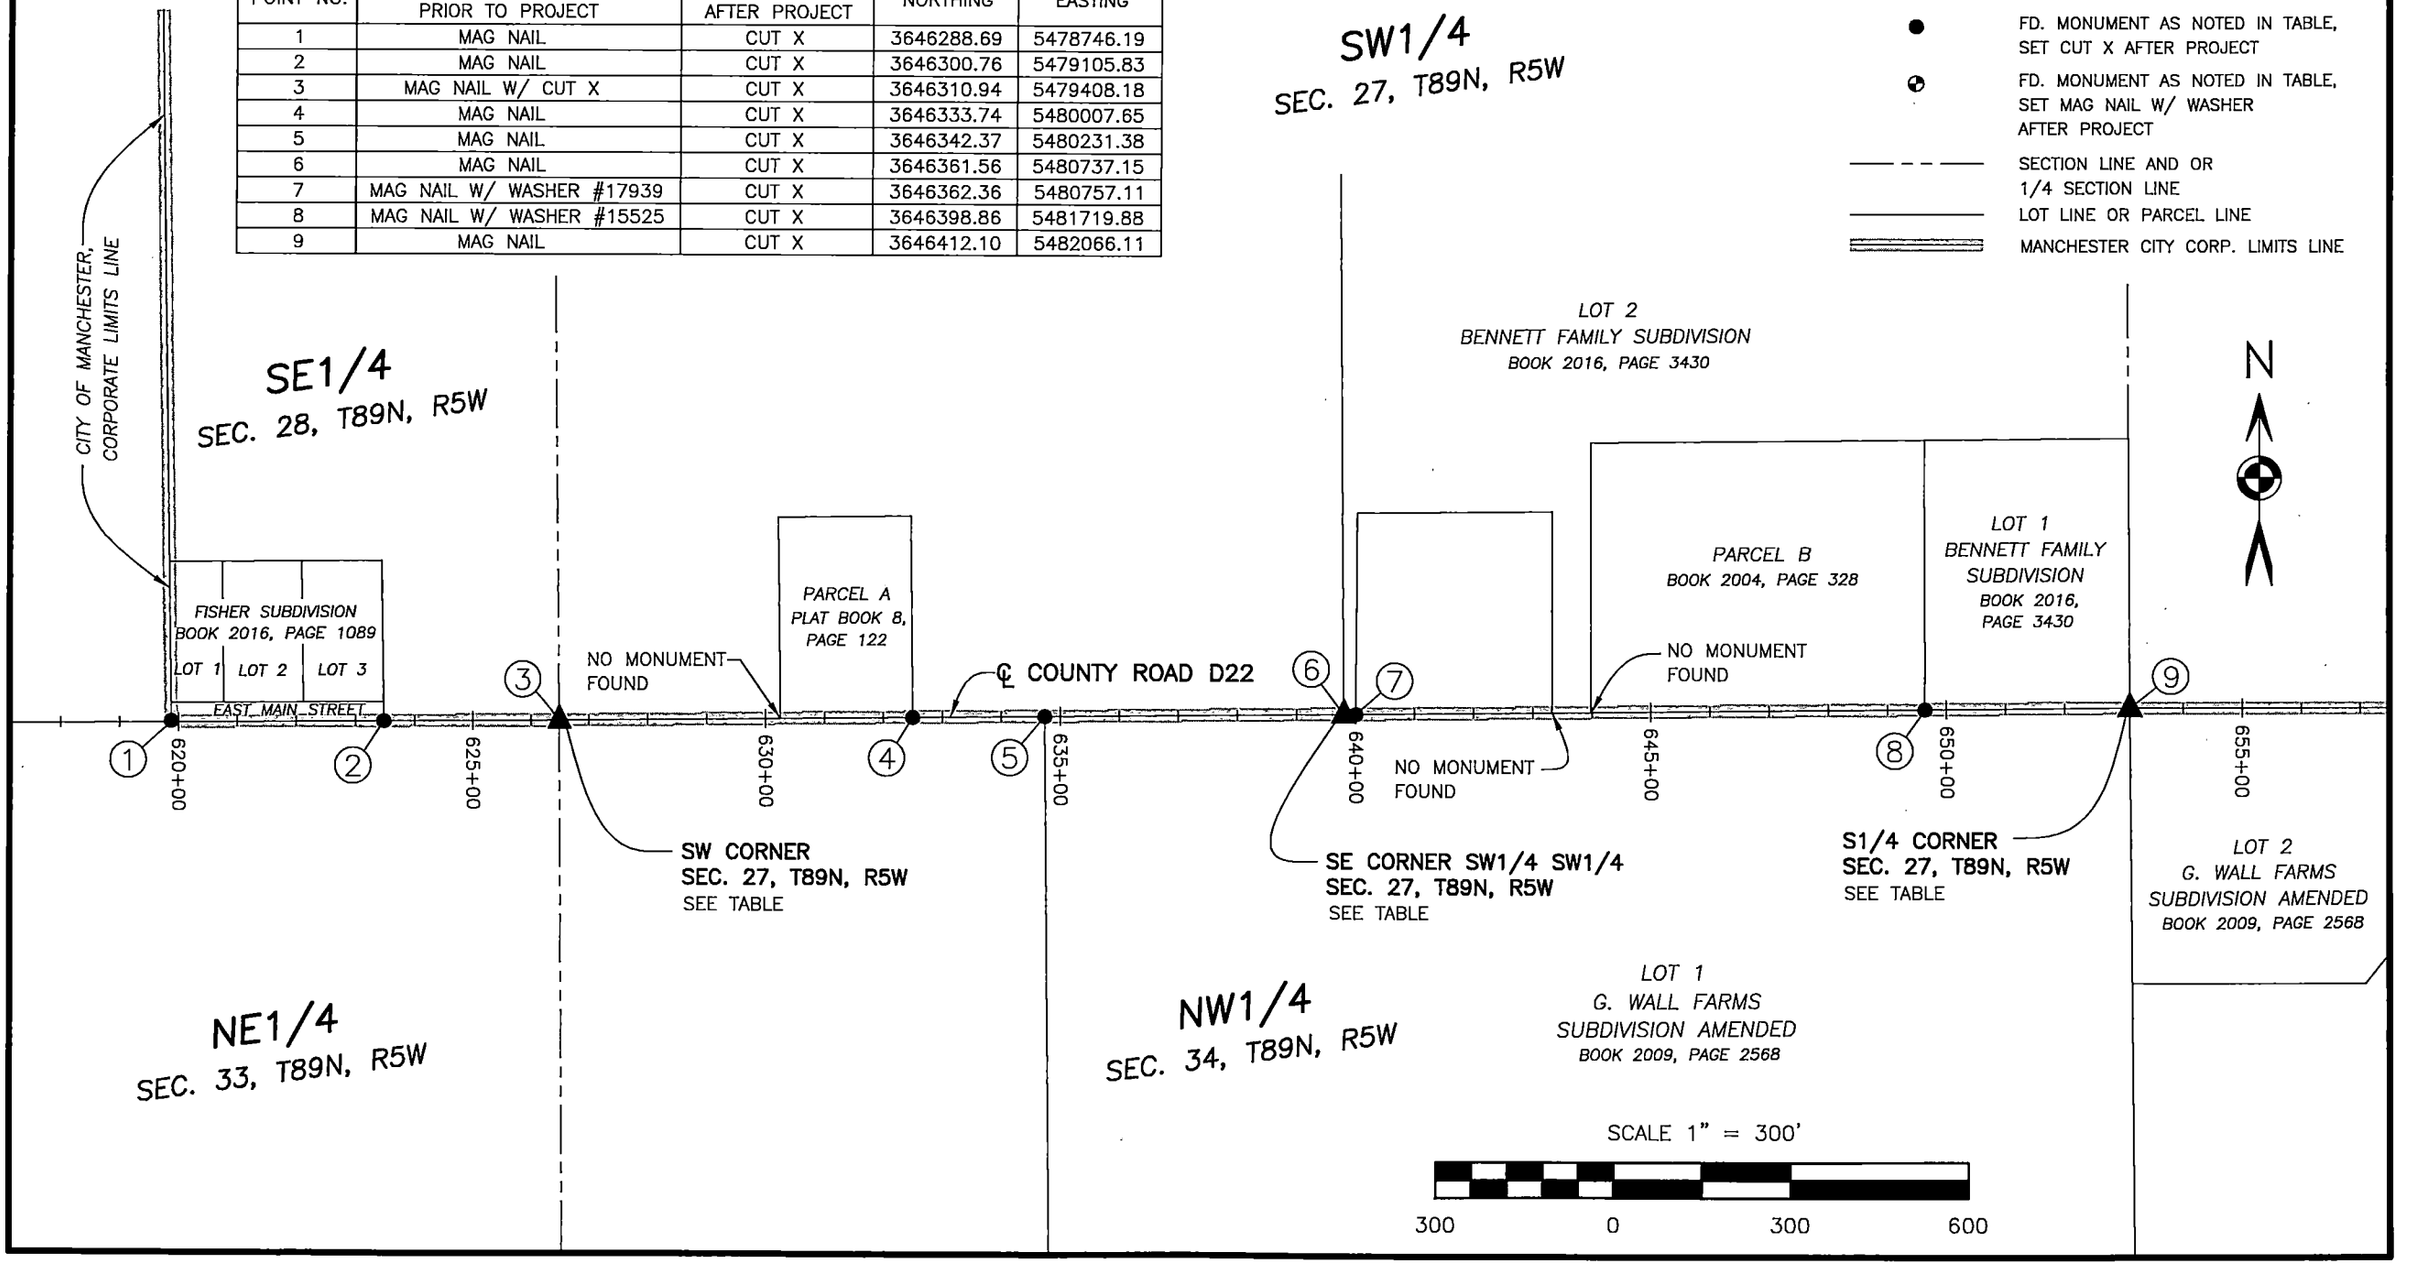

MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
10	MAG NAIL	CUT X	3646426.12	5482580.76
11	MAG NAIL W/ WASHER	CUT X	3646448.13	5483388.04
12	MAG NAIL	CUT X	3646454.15	5483612.97
13	MAG NAIL	CUT X	3646484.22	5484728.60
14	MAG NAIL	CUT X	3646530.07	5486039.70

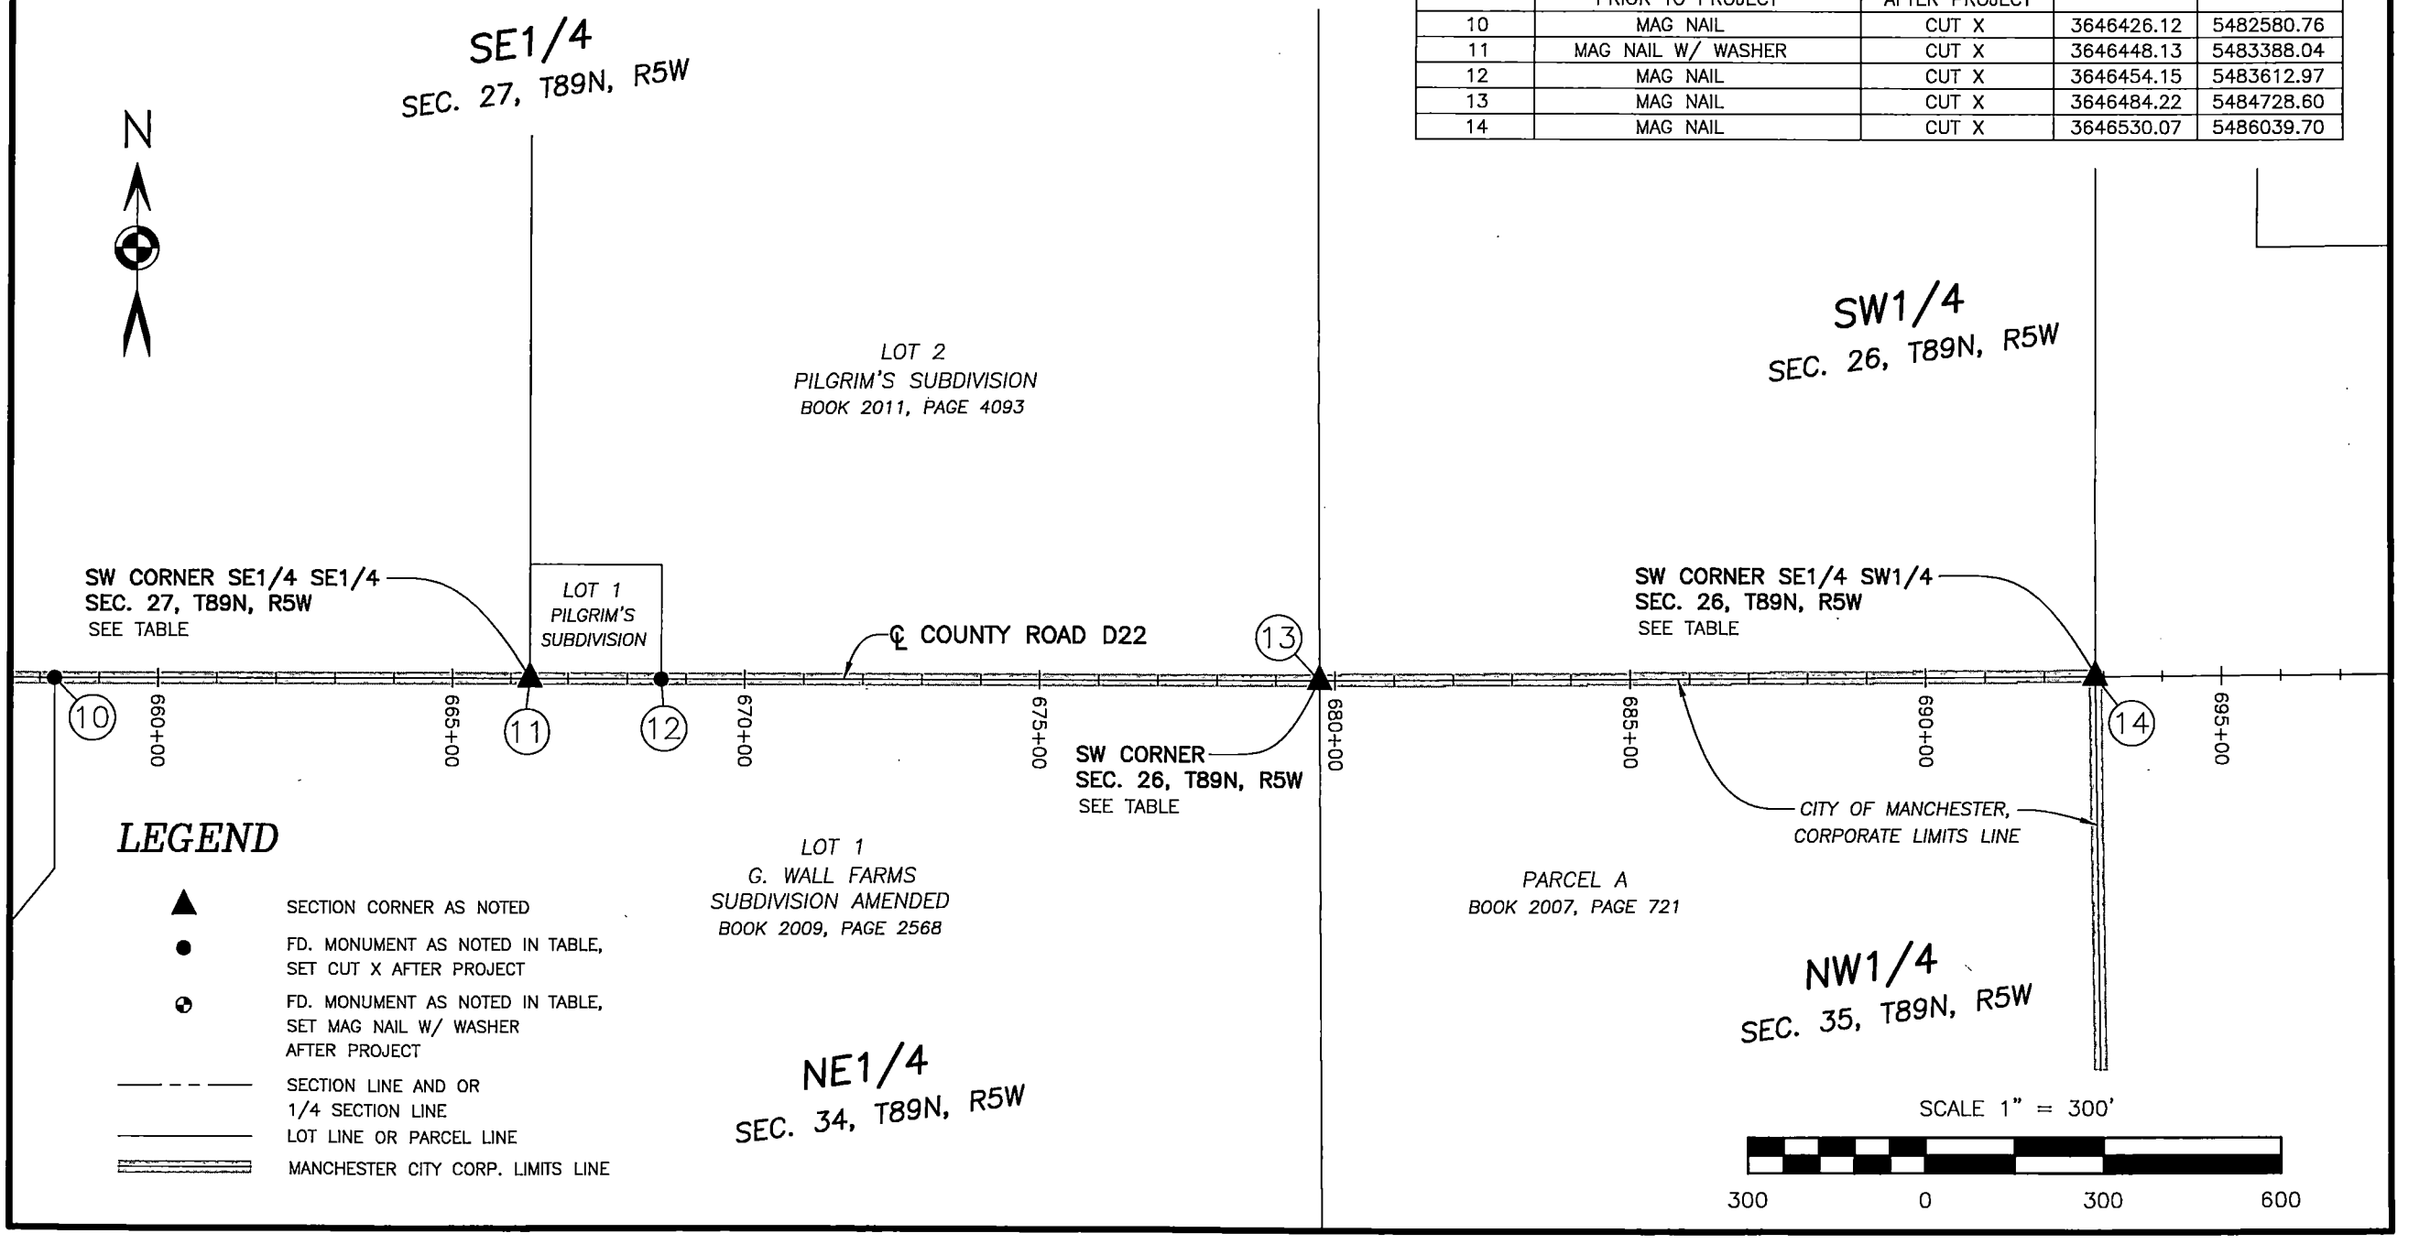


MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
15	MAG NAIL	CUT X	3646576.23	5487361.36
16	MAG NAIL W/ WASHER	CUT X	3646578.35	5487456.38
17	MAG NAIL	CUT X	3646636.23	5489997.59

LEGEND

- ▲ SECTION CORNER AS NOTED
- ● FD. MONUMENT AS NOTED IN TABLE, SET CUT X AFTER PROJECT
- ◒ FD. MONUMENT AS NOTED IN TABLE, SET MAG NAIL W/ WASHER AFTER PROJECT
- ——— SECTION LINE AND OR 1/4 SECTION LINE
- ——— LOT LINE OR PARCEL LINE

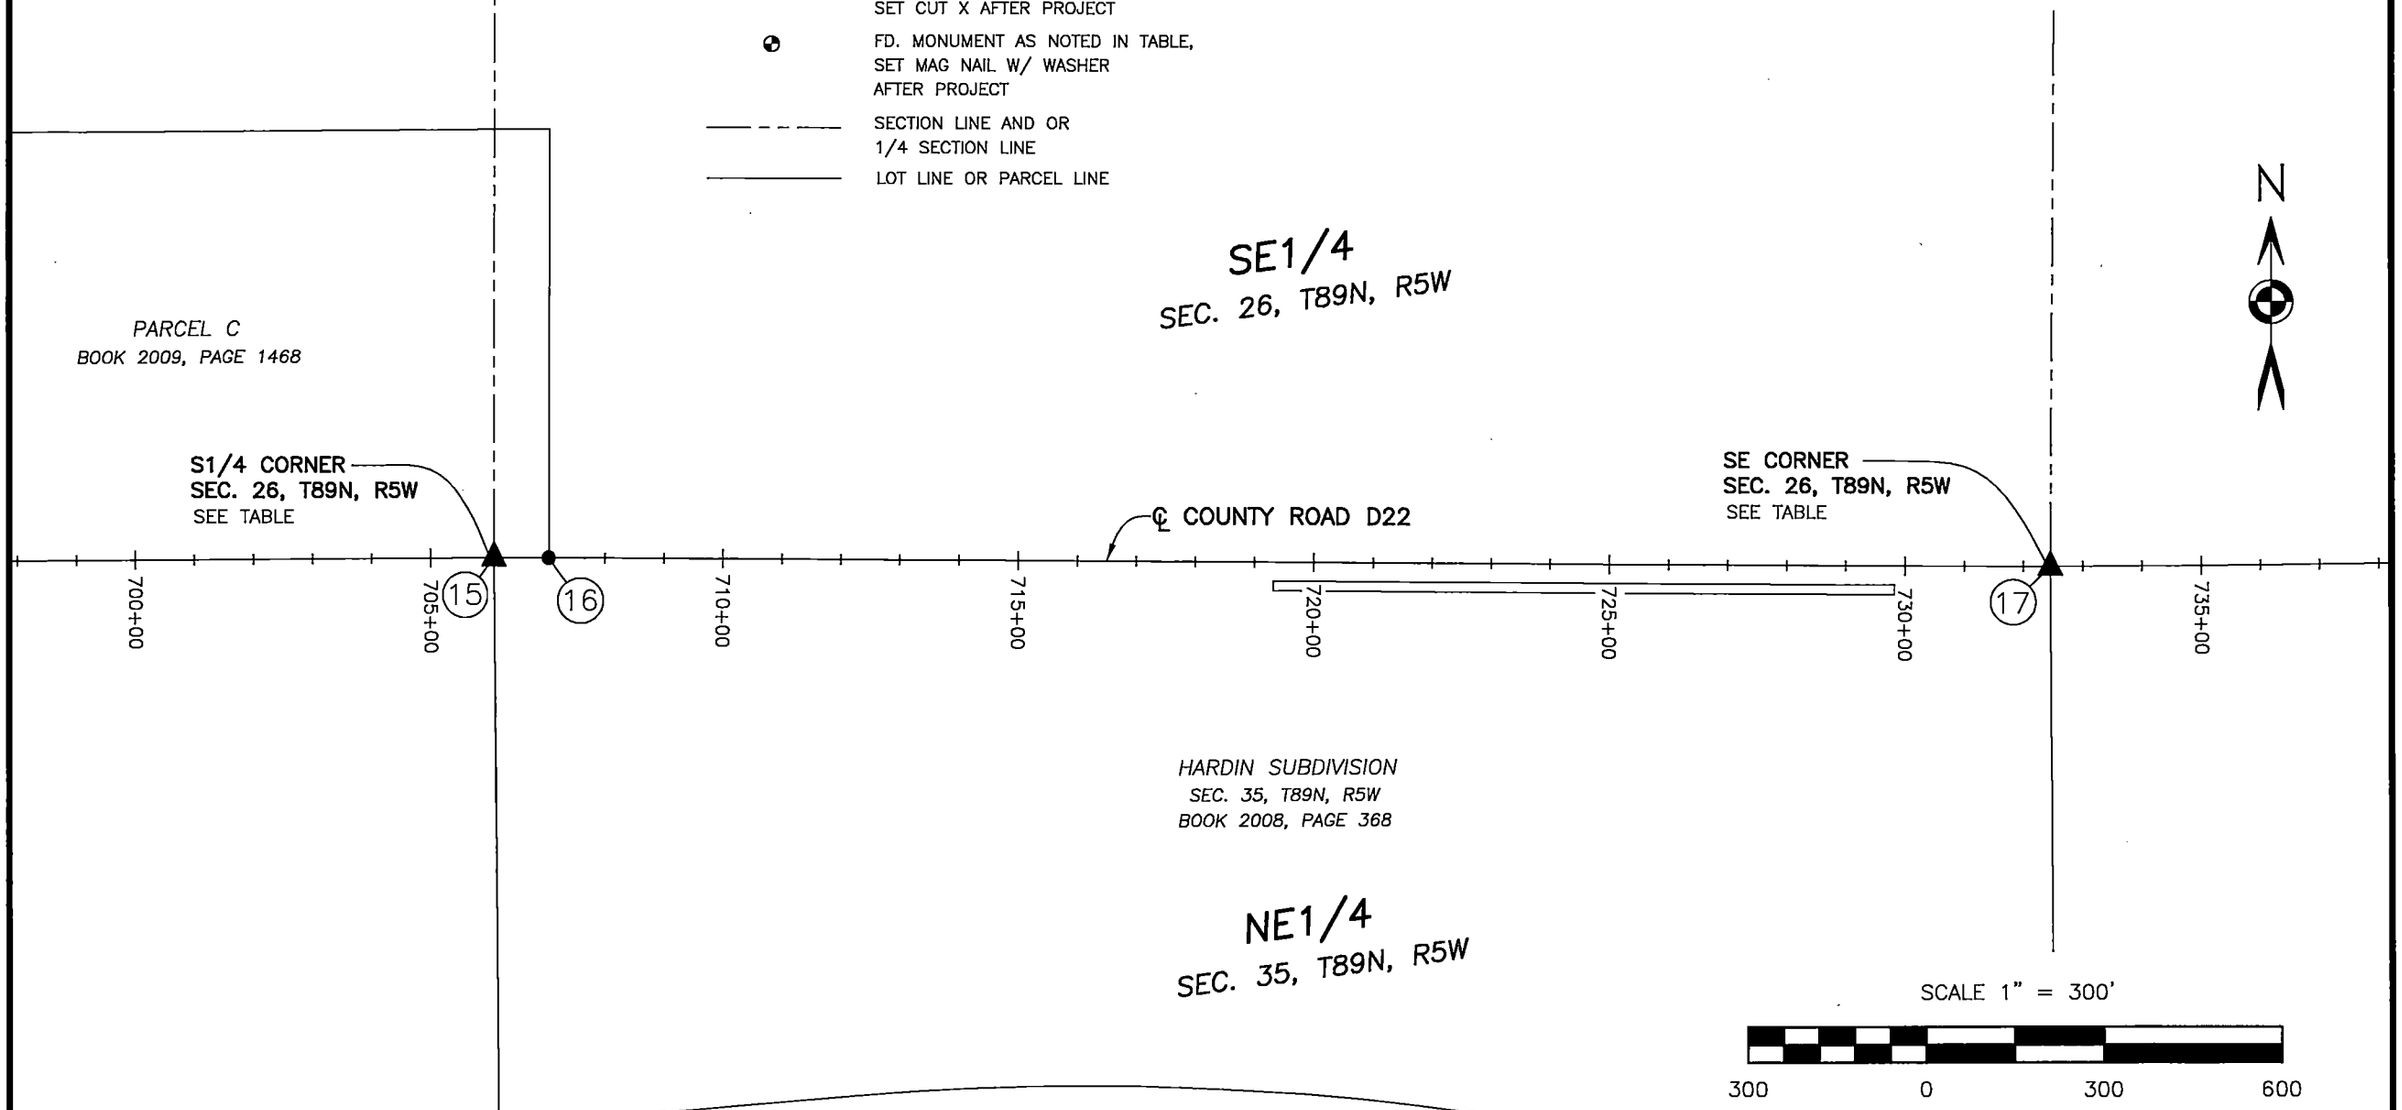


MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
18	CUT X IN ASPHALT	CUT X	3646737.78	5492615.95
19	MAG NAIL	CUT X	3646745.91	5492825.75
20	BROKEN OFF MAG NAIL	CUT X	3646748.50	5492891.67
21	MAG NAIL	CUT X	3646756.72	5493101.56
22	MAG NAIL W/ WASHER #10165	CUT X	3646760.00	5493182.98
23	MAG NAIL	CUT X	3646773.23	5493522.18
24	MAG NAIL W/ WASHER	CUT X	3646802.29	5494257.59
25	MAG NAIL W/ WASHER	CUT X	3646812.37	5494514.73
26	MAG NAIL	CUT X	3646813.61	5494547.71


LEGEND

- SECTION CORNER AS NOTED
- FD. MONUMENT AS NOTED IN TABLE, SET CUT X AFTER PROJECT
- FD. MONUMENT AS NOTED IN TABLE, SET MAG NAIL W/ WASHER AFTER PROJECT
- SECTION LINE AND OR 1/4 SECTION LINE
- LOT LINE OR PARCEL LINE

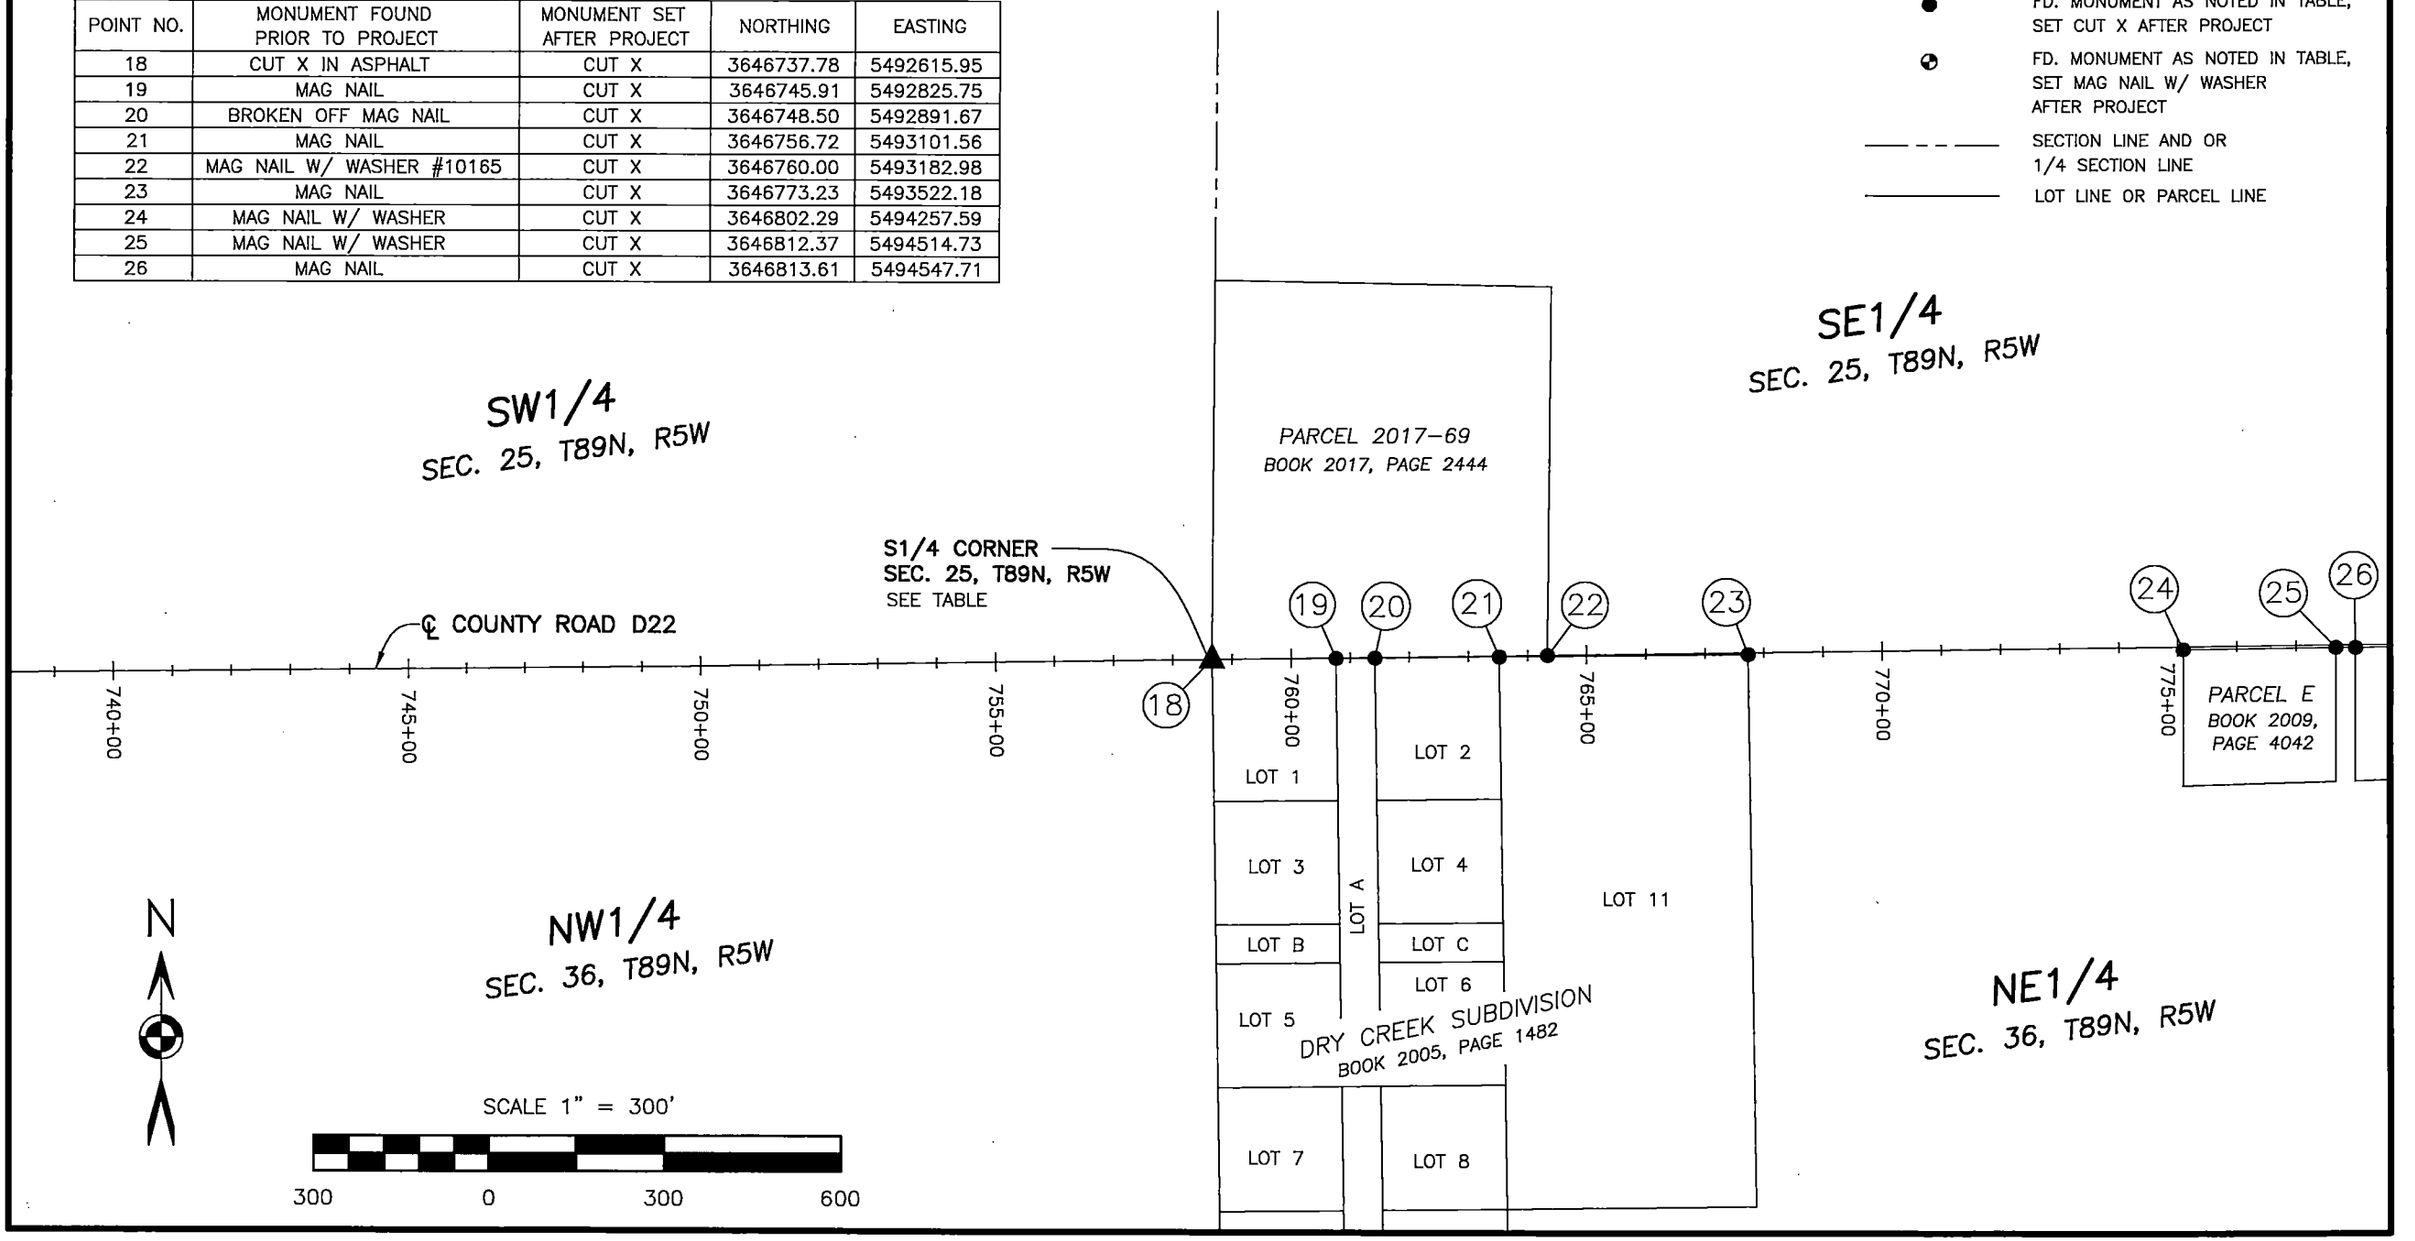

MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
27	MAG NAIL W/ WASHER	CUT X	3646828.11	5494902.50
28	MAG NAIL W/ WASHER #7060	CUT X	3646857.96	5495822.03
29	MAG NAIL W/ WASHER #7060	CUT X	3646870.96	5496276.83
30	MAG NAIL W/ WASHER #7060	CUT X	3646884.04	5496737.47
31	MAG NAIL W/ WASHER #7060	CUT X	3646914.54	5497802.75
32	BROKEN OFF MAG NAIL	CUT X	3646922.37	5498075.21
33	BROKEN OFF MAG NAIL	CUT X	3646923.30	5498108.21
34	BROKEN OFF MAG NAIL	CUT X	3646924.28	5498141.18
35	MAG NAIL	CUT X	3646933.36	5498466.08

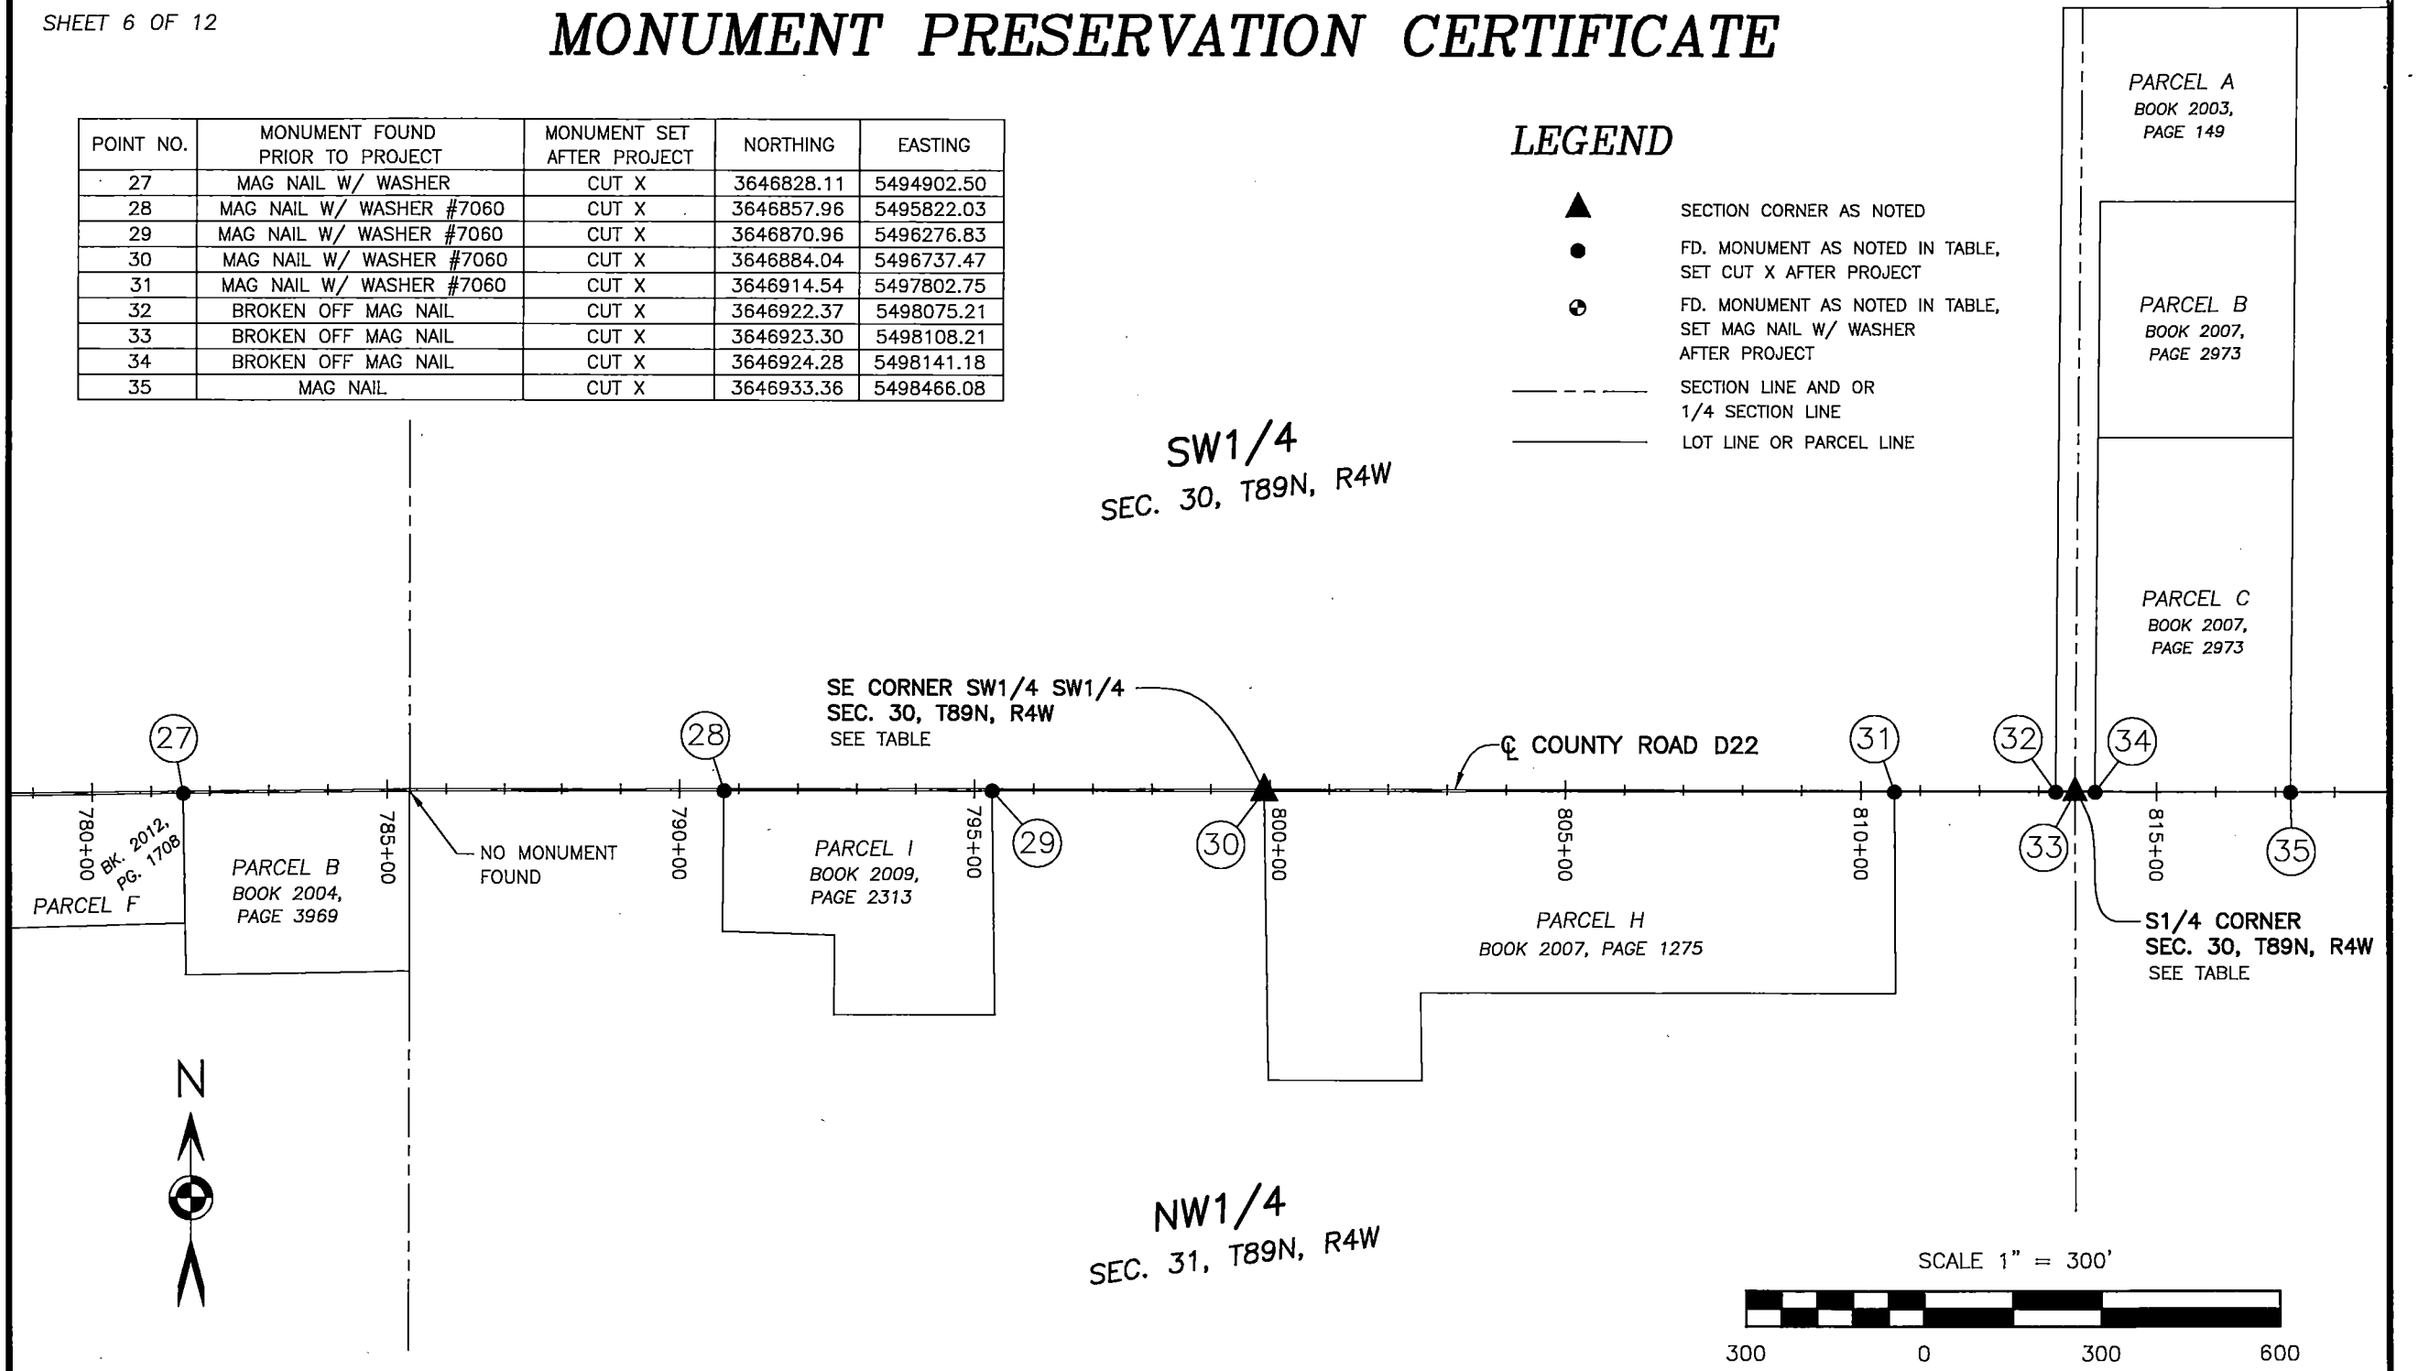


MONUMENT PRESERVATION CERTIFICATE


LEGEND

- ▲ SECTION CORNER AS NOTED
- ● FD. MONUMENT AS NOTED IN TABLE, SET CUT X AFTER PROJECT
- ⊕ FD. MONUMENT AS NOTED IN TABLE, SET MAG NAIL W/ WASHER AFTER PROJECT
- — — — SECTION LINE AND OR 1/4 SECTION LINE
- ——— LOT LINE OR PARCEL LINE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
36	MAG NAIL	CUT X	3646952.46	5499136.70
37	BROKEN OFF MAG NAIL	CUT X	3646960.92	5499427.60
38	MAG NAIL	CUT X	3646969.77	5499737.52
39	BROKEN OFF MAG NAIL	CUT X	3646971.21	5499787.39
40	MAG NAIL	CUT X	3646990.80	5500477.16
41	MAG NAIL	CUT X	3646998.49	5500746.89
42	BROKEN OFF MAG NAIL	CUT X	3647054.17	5502065.00

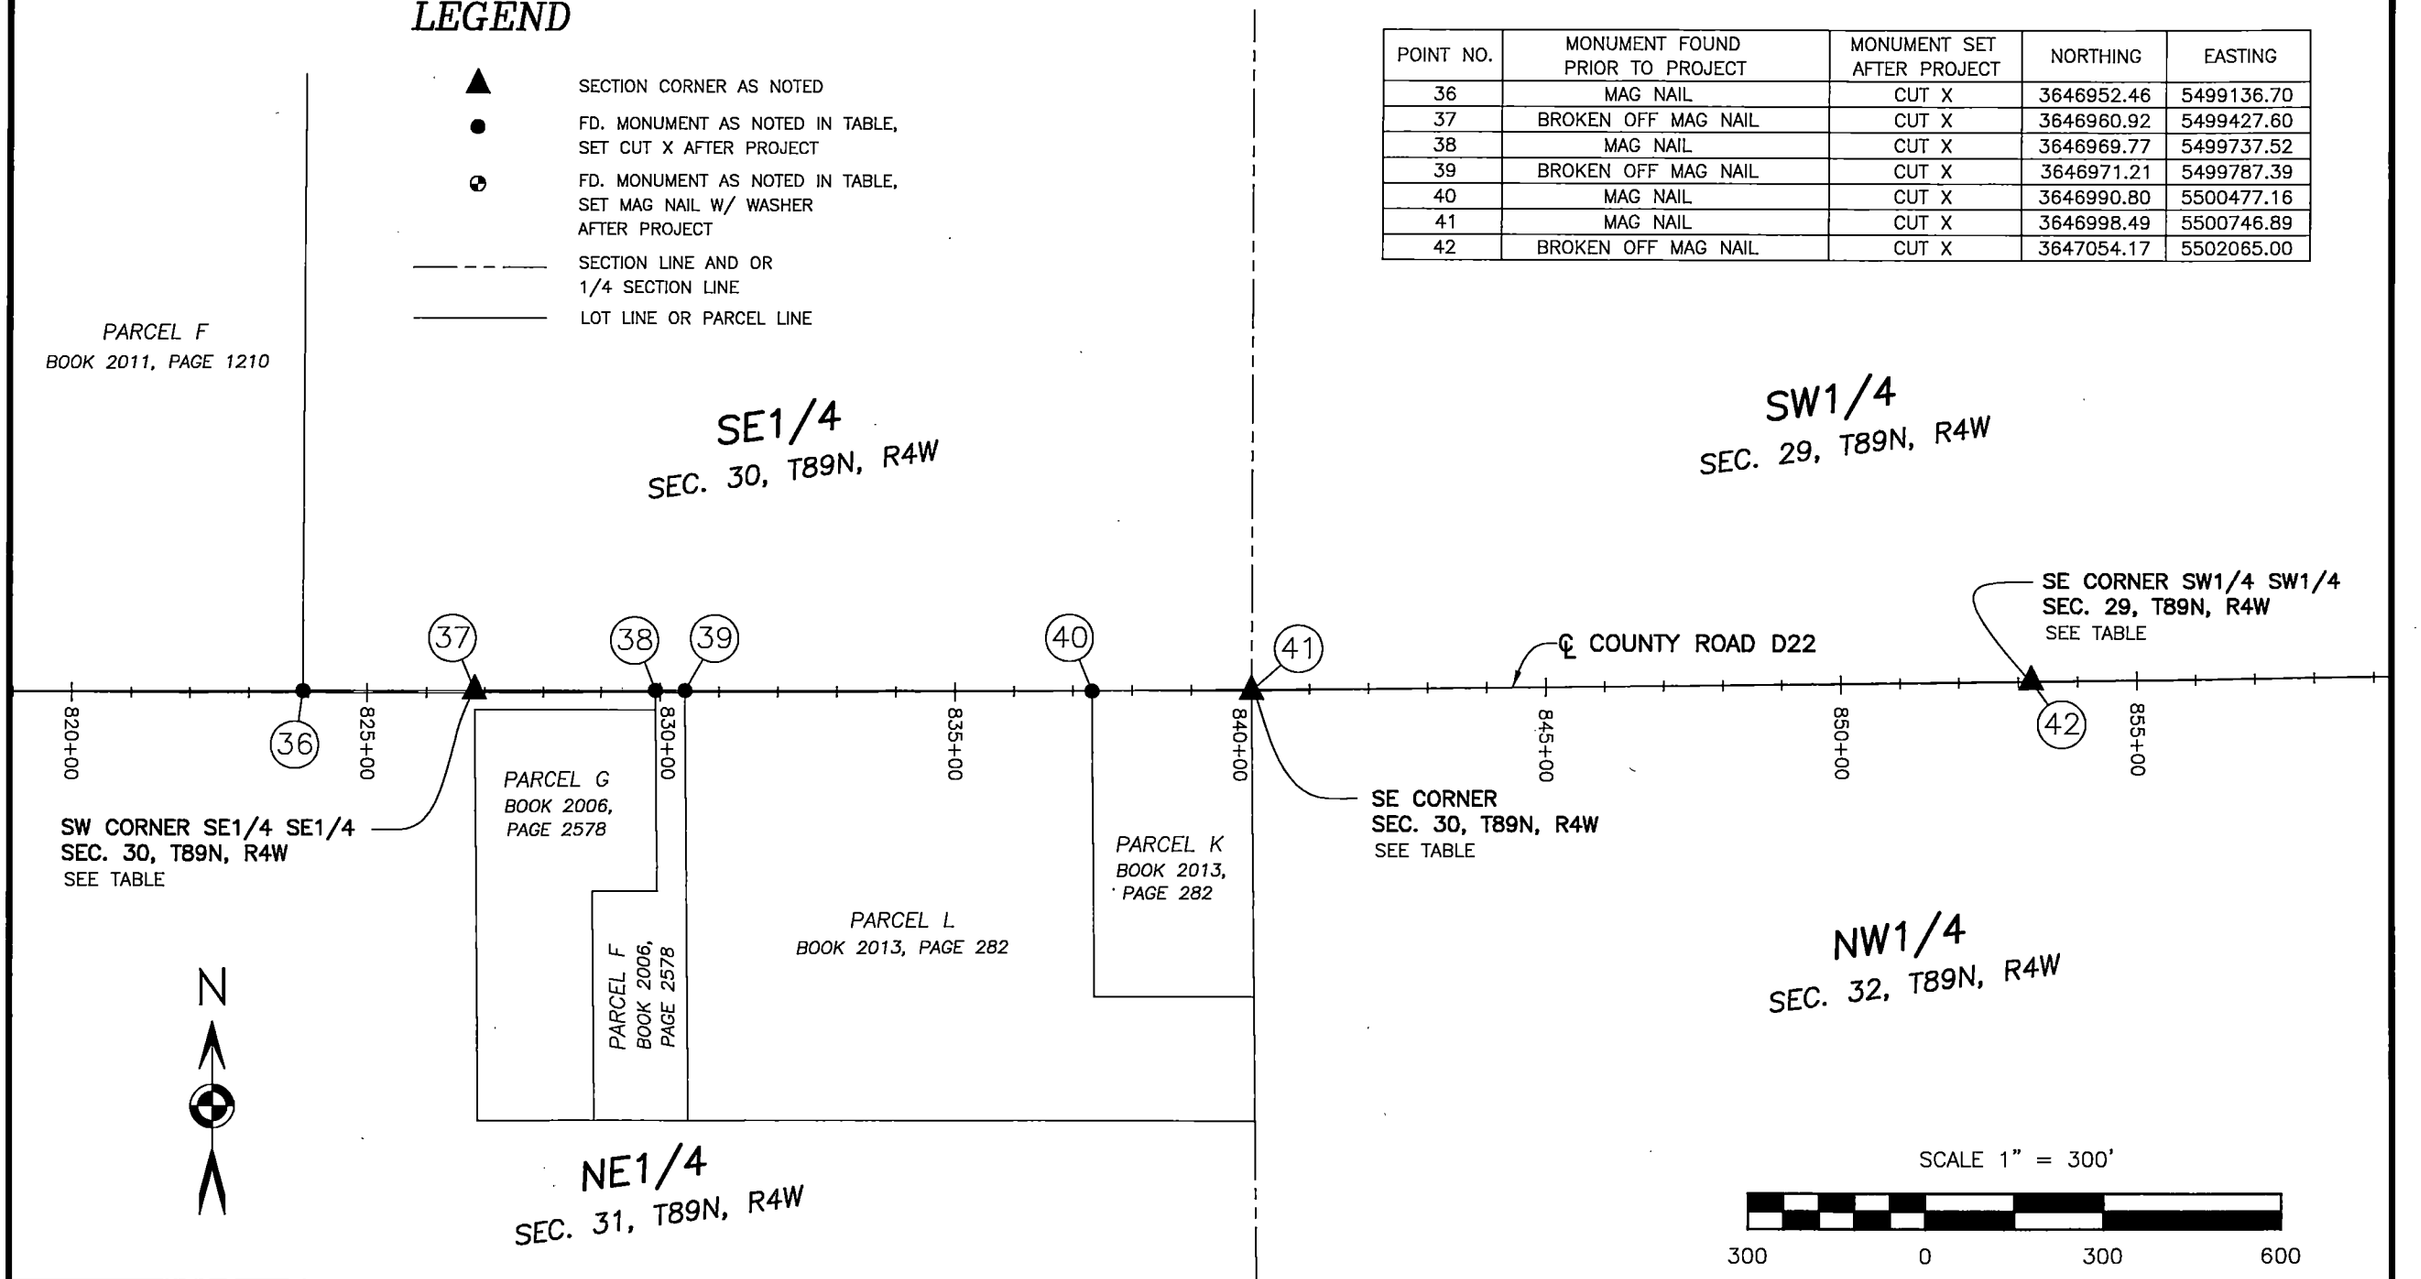

MONUMENT PRESERVATION CERTIFICATE

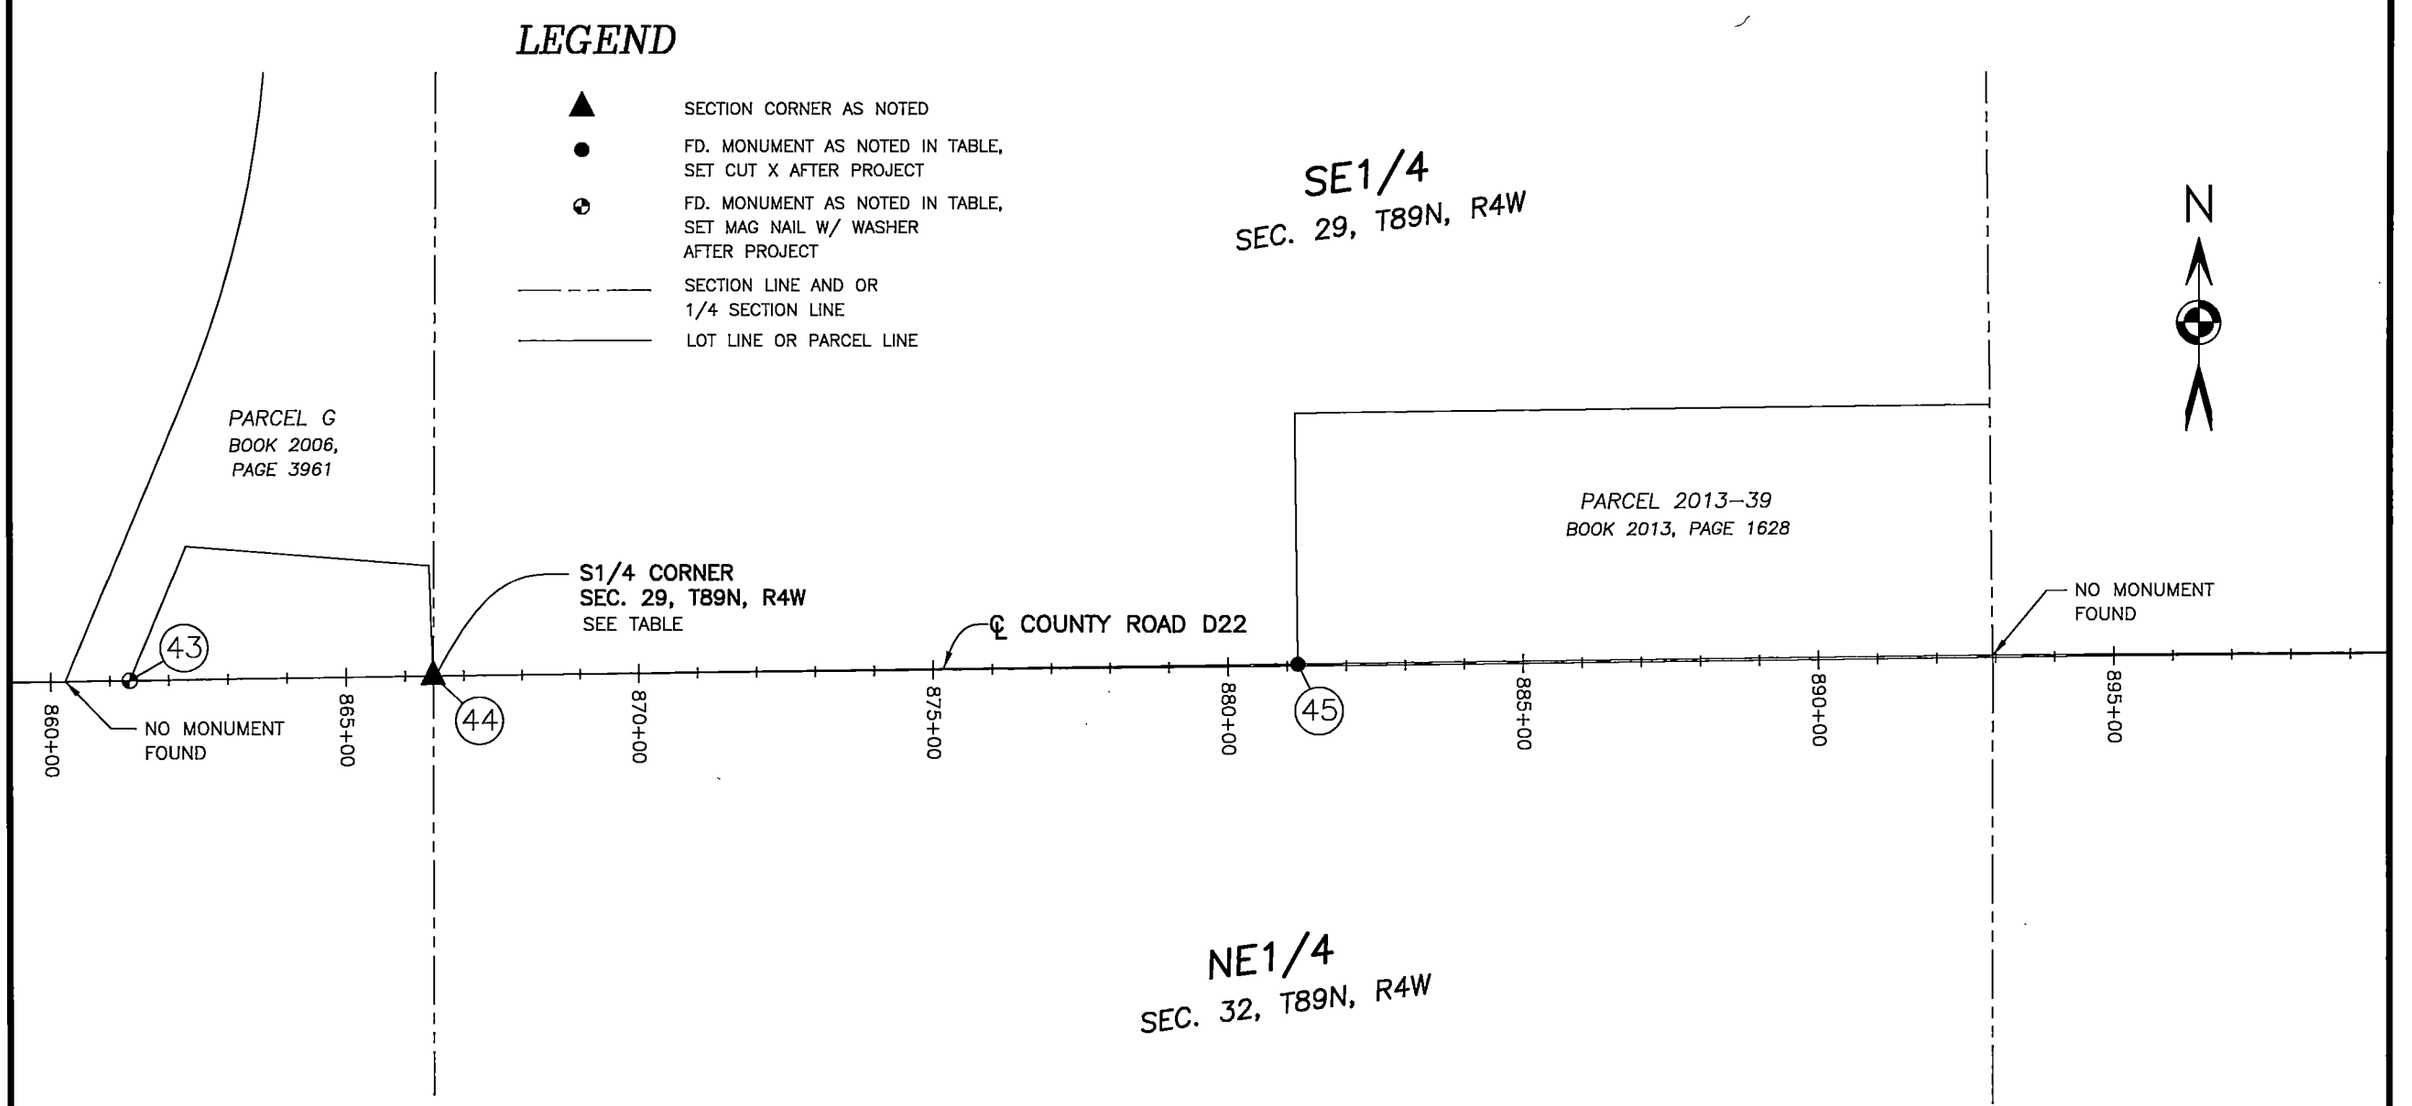


POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
43	MAG NAIL	MAG NAIL W/ WASHER	3647087.06	5502876.51
44	CUT X IN ASPHALT	MAG NAIL W/ WASHER	3647107.92	5503389.82
45	MAG NAIL	CUT X	3647167.40	5504859.03

SCALE 1" = 300'

300 0 300 600

MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
46	MAG NAIL W/ WASHER #8419	CUT X	3647312.73	5508667.36

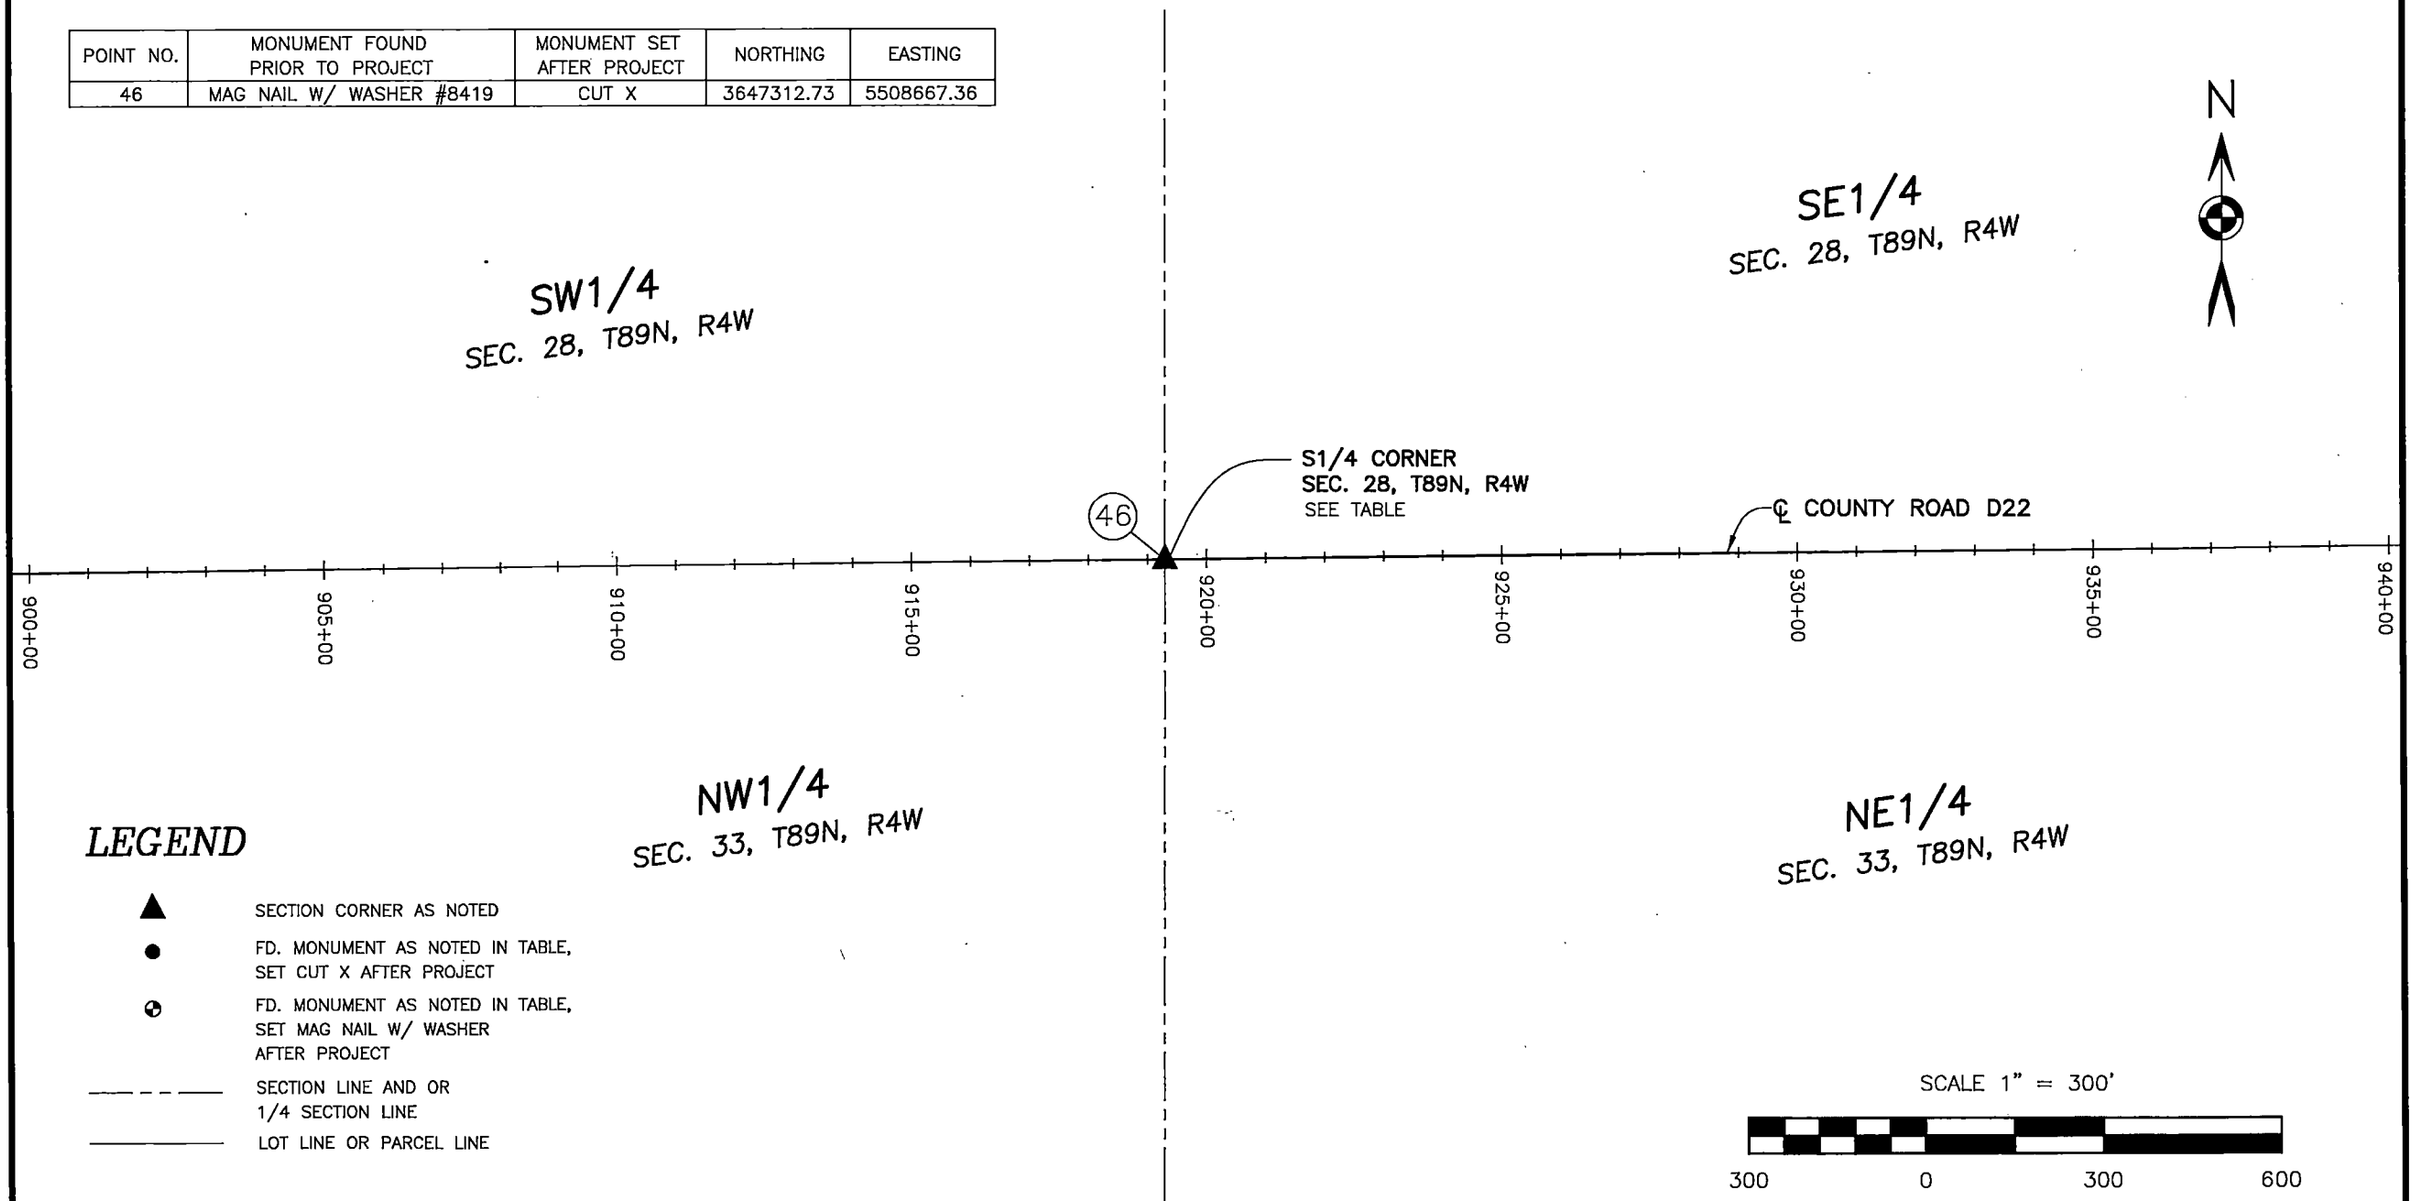

LEGEND


- ▲ SECTION CORNER AS NOTED
- ● FD. MONUMENT AS NOTED IN TABLE, SET CUT X AFTER PROJECT
- ⊕ FD. MONUMENT AS NOTED IN TABLE, SET MAG NAIL W/ WASHER AFTER PROJECT
- — — — SECTION LINE AND OR 1/4 SECTION LINE
- ——— LOT LINE OR PARCEL LINE

SCALE 1" = 300'


300 0 300 600

MONUMENT PRESERVATION CERTIFICATE

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
47	MAG NAIL W/ CUT X	CUT X	3647412.00	5511305.52

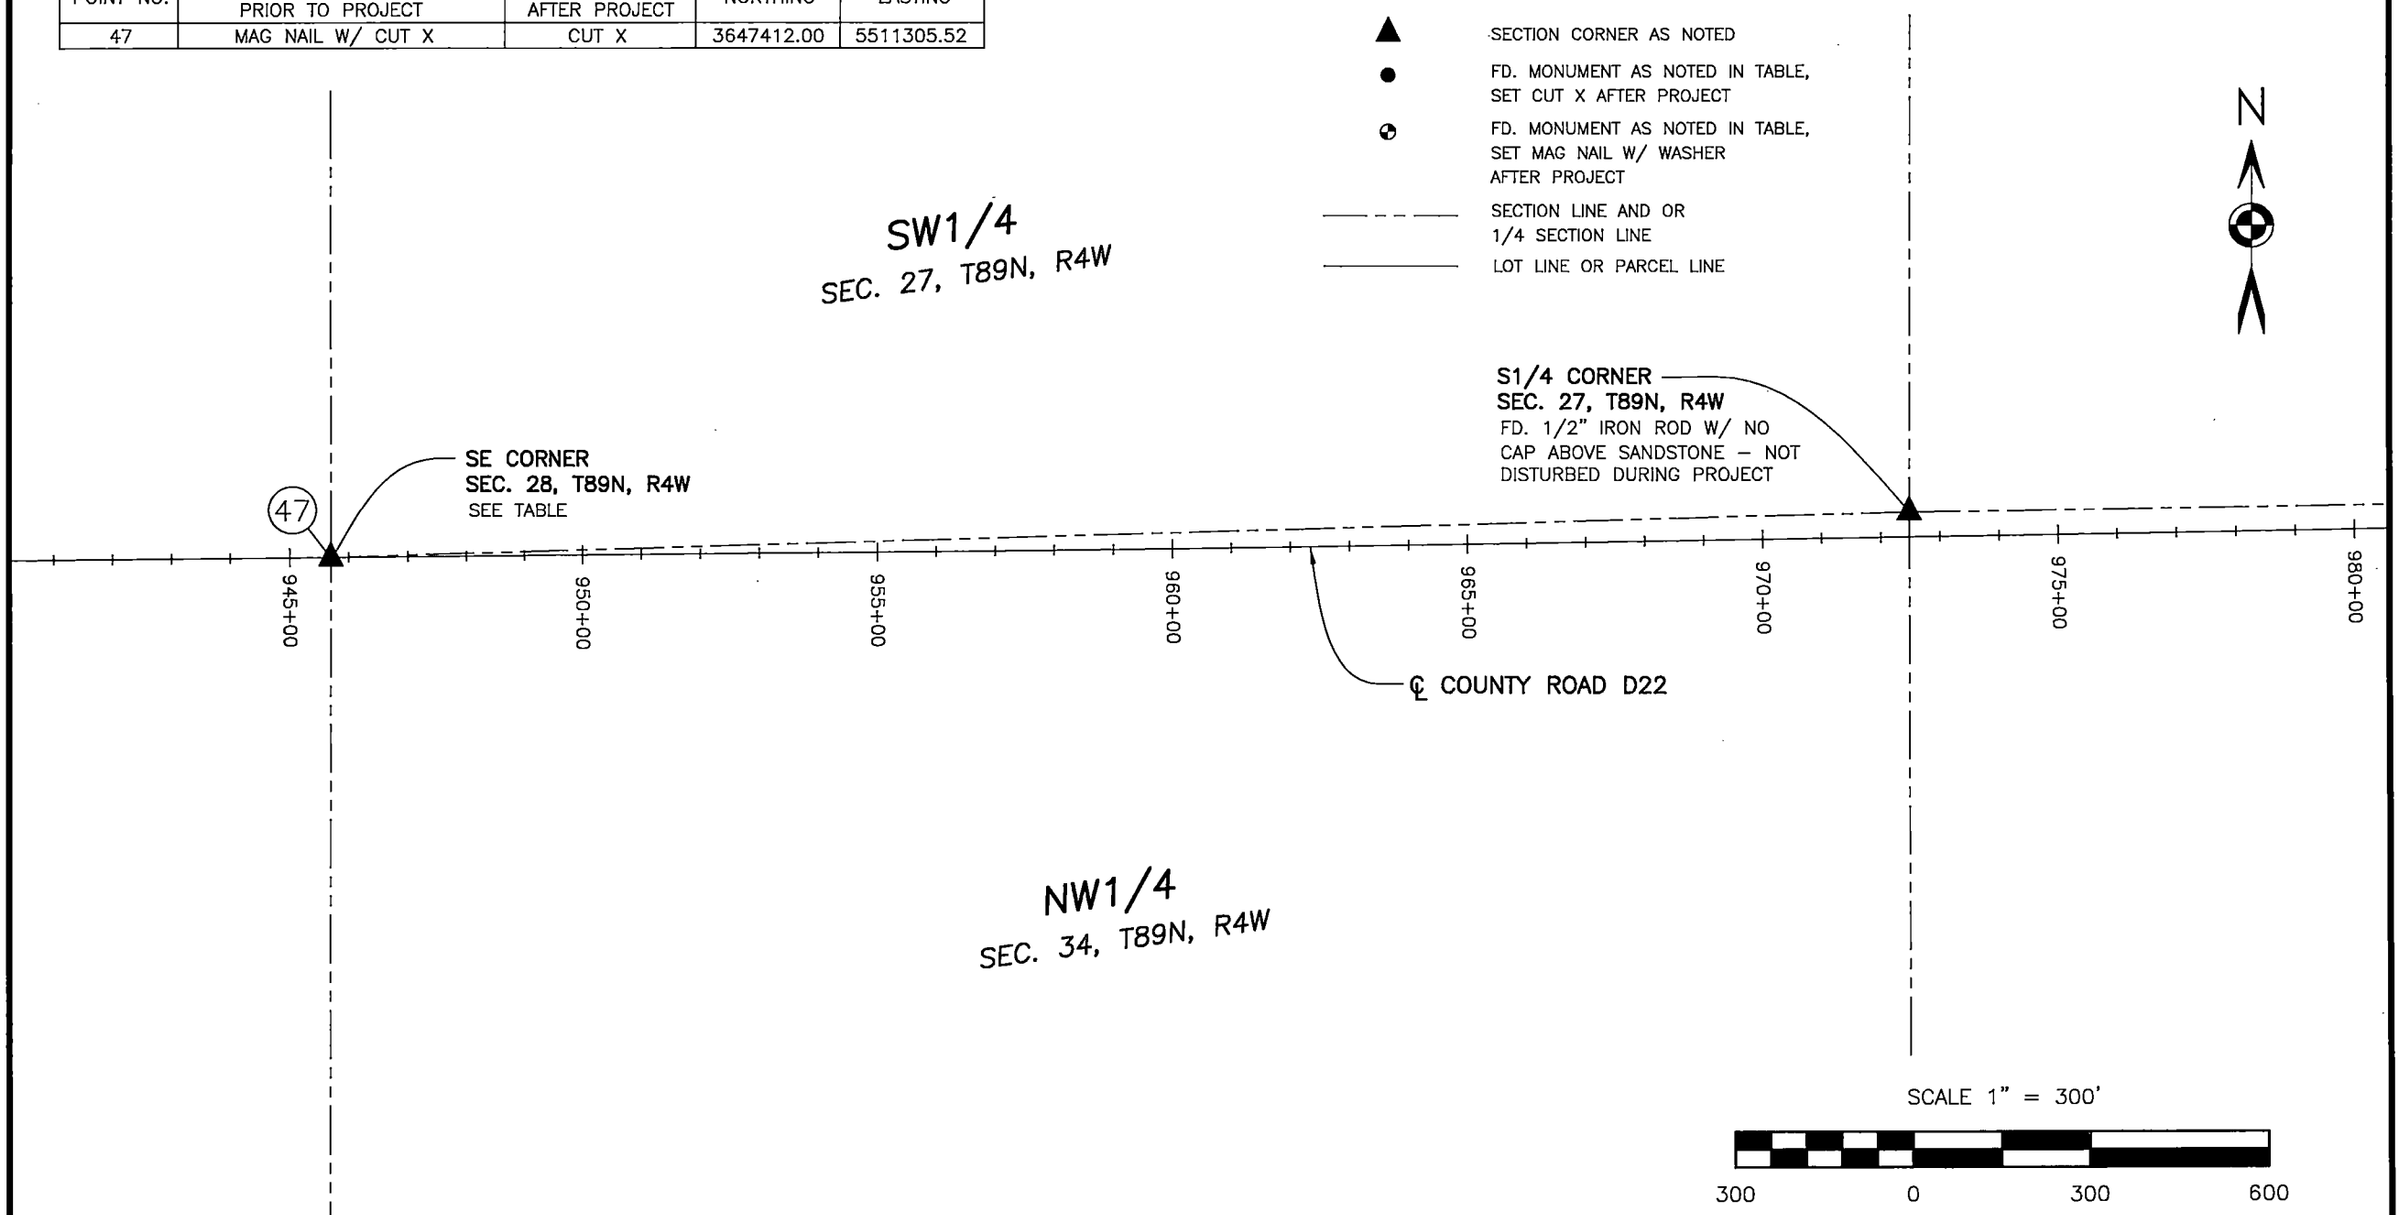


MONUMENT PRESERVATION CERTIFICATE

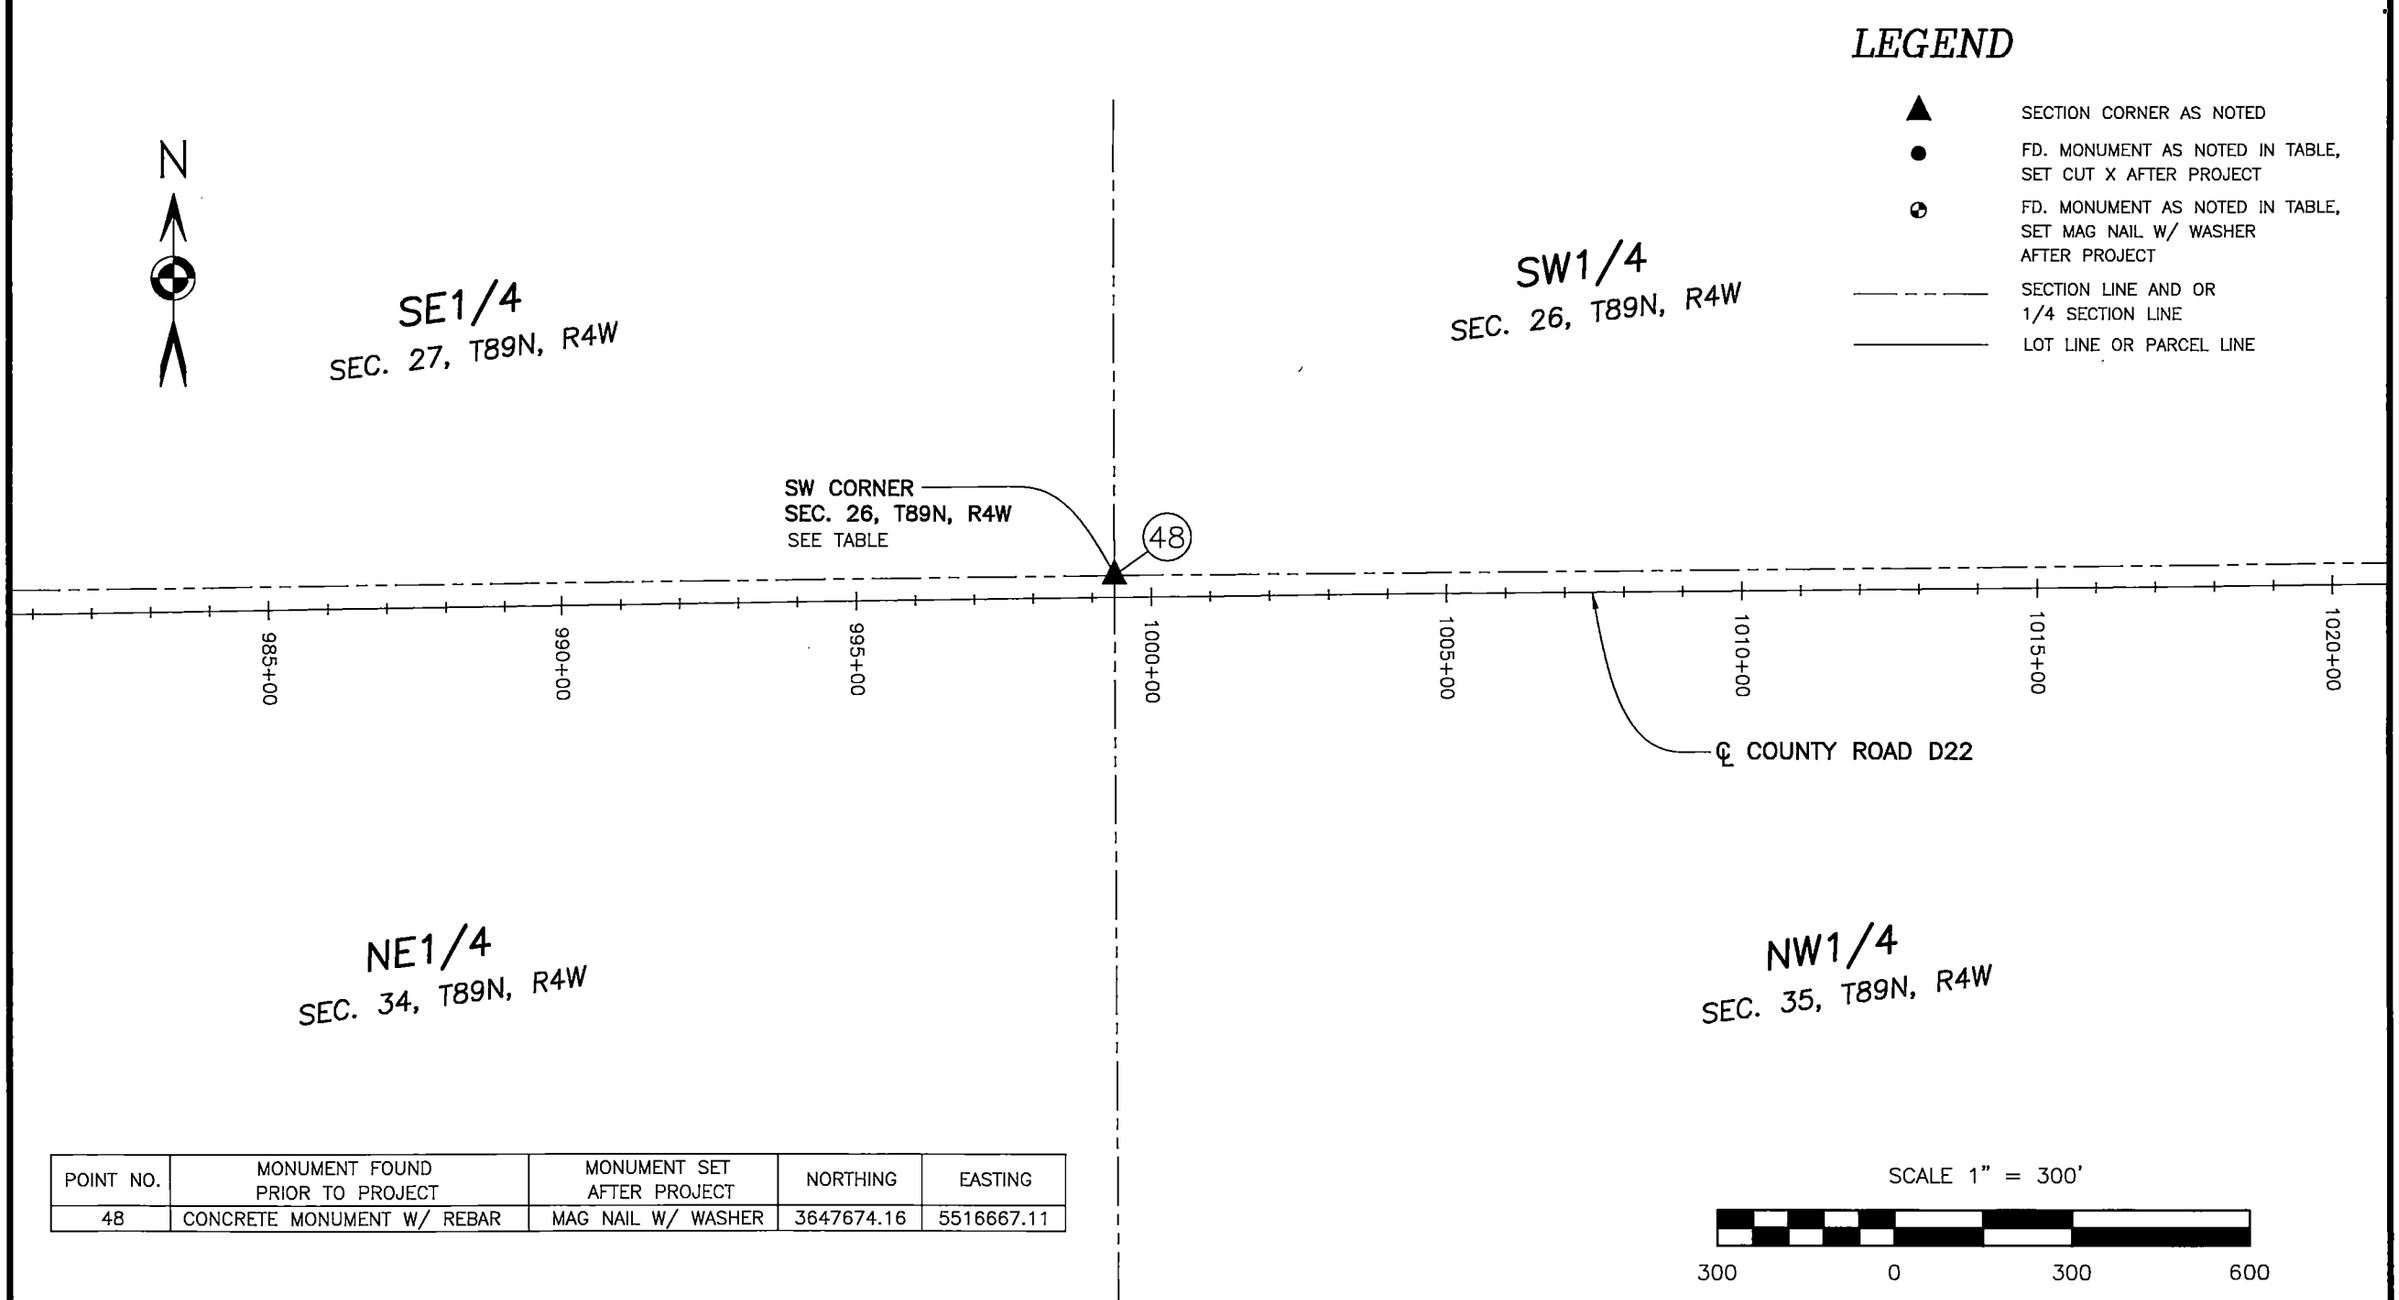

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
48	CONCRETE MONUMENT W/ REBAR	MAG NAIL W/ WASHER	3647674.16	5516667.11

MONUMENT PRESERVATION CERTIFICATE

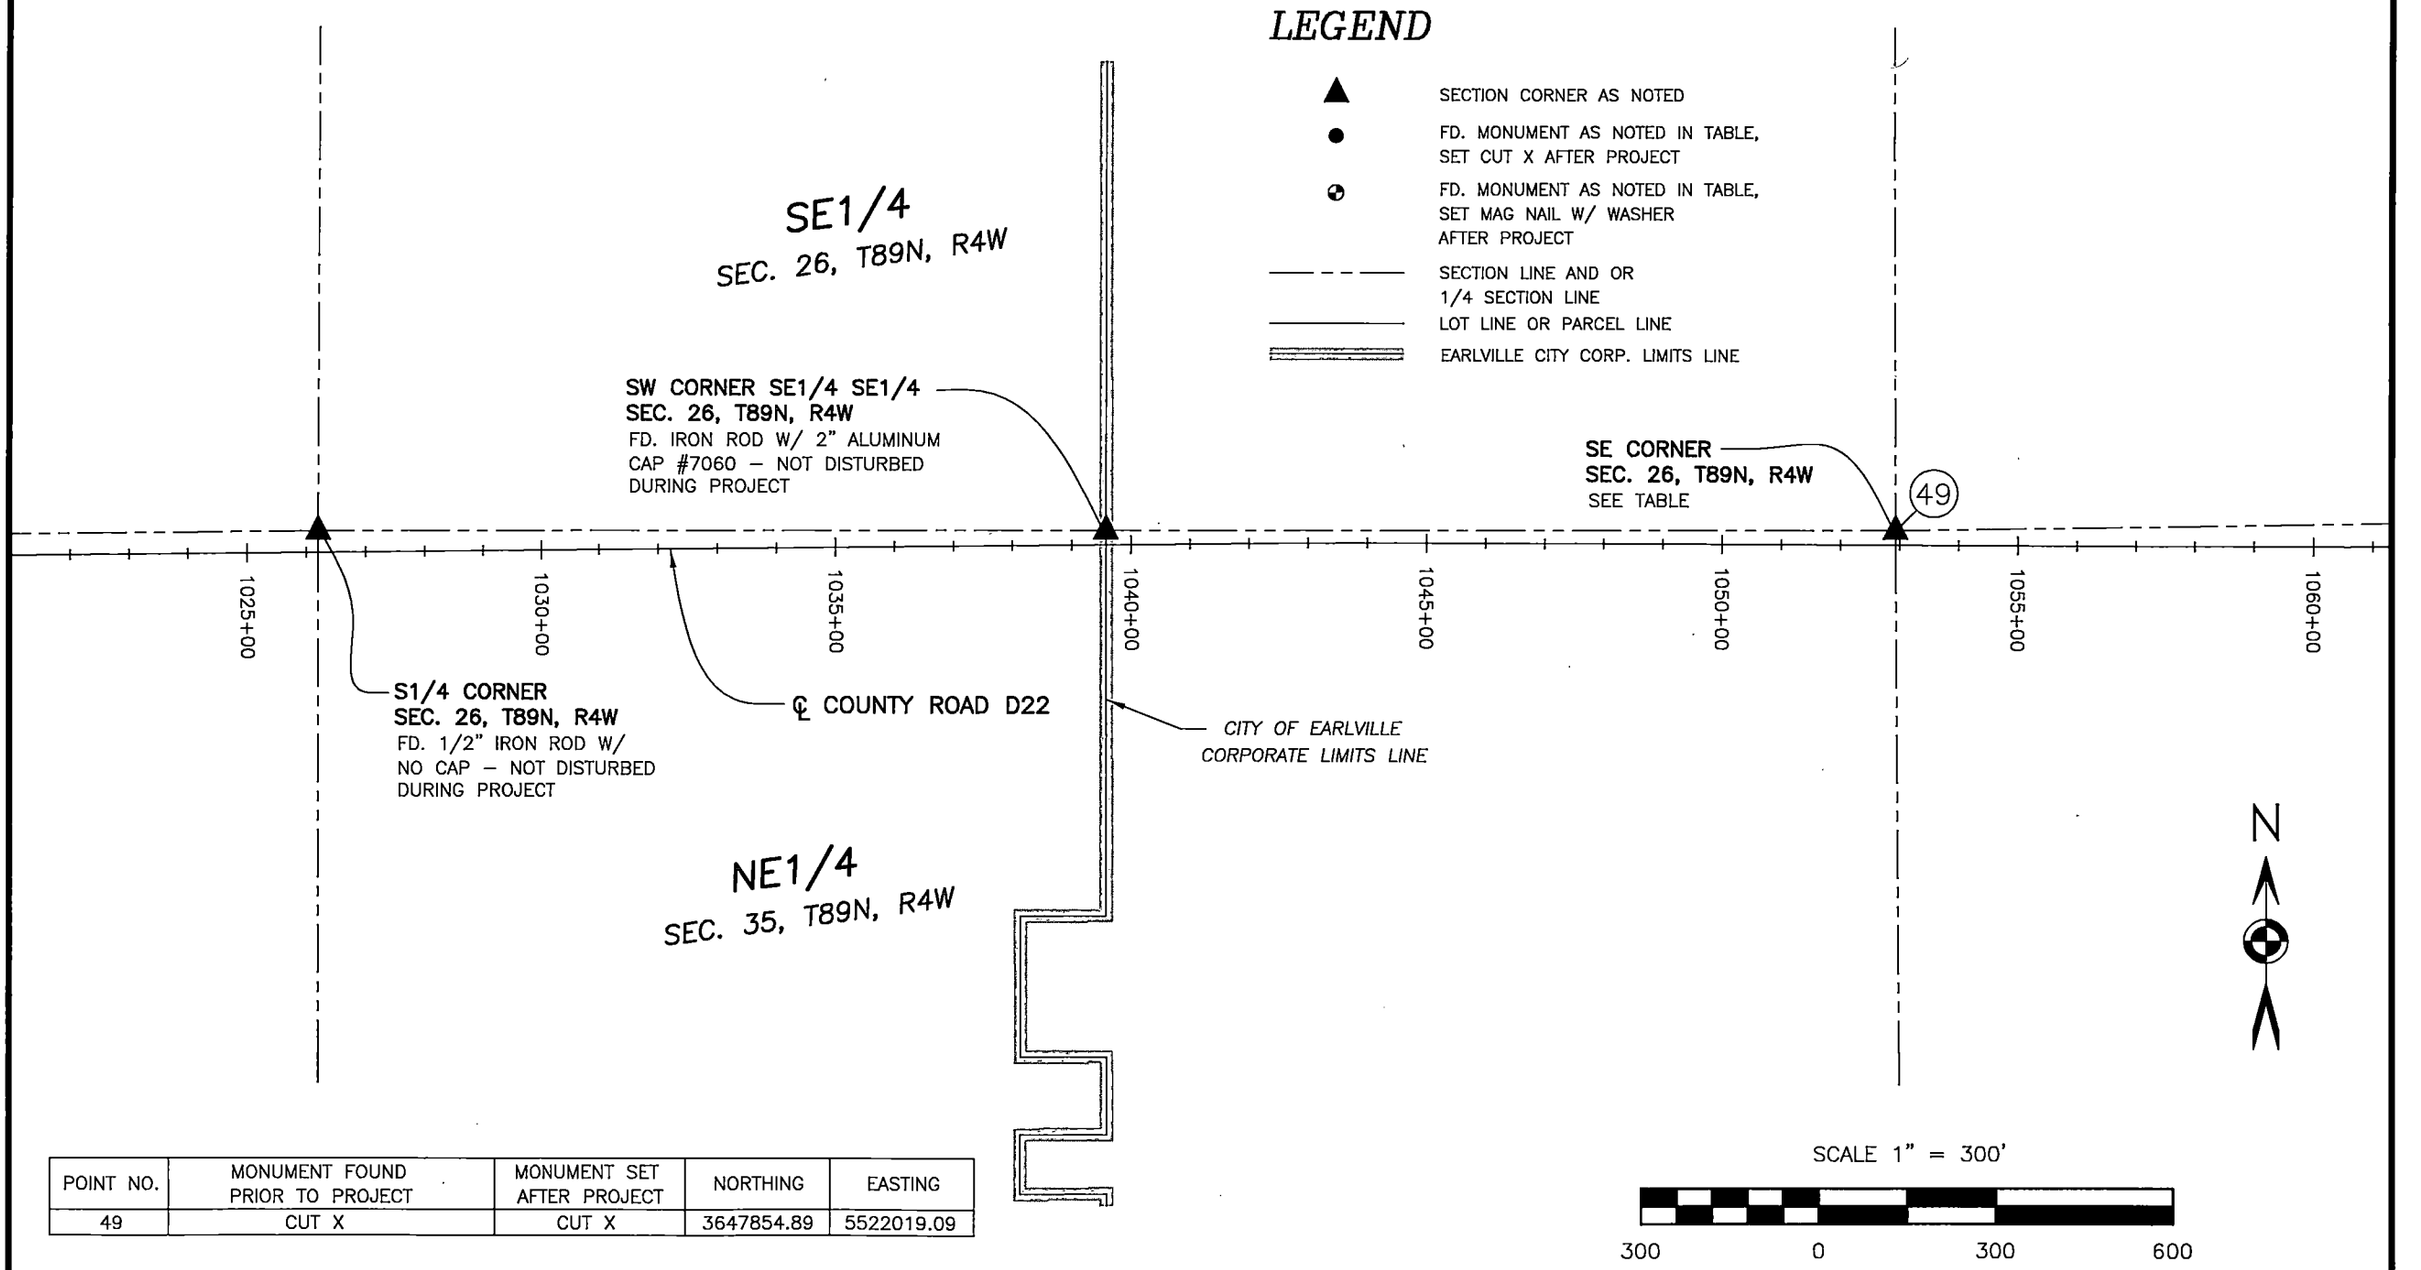

POINT NO.	MONUMENT FOUND PRIOR TO PROJECT	MONUMENT SET AFTER PROJECT	NORTHING	EASTING
49	CUT X	CUT X	3647854.89	5522019.09
